


Option 6 – Phase 3

- Construction of SB Carriageway overlay
- Traffic in Dual Contraflow on NB Carriageway
- Access to farm house required

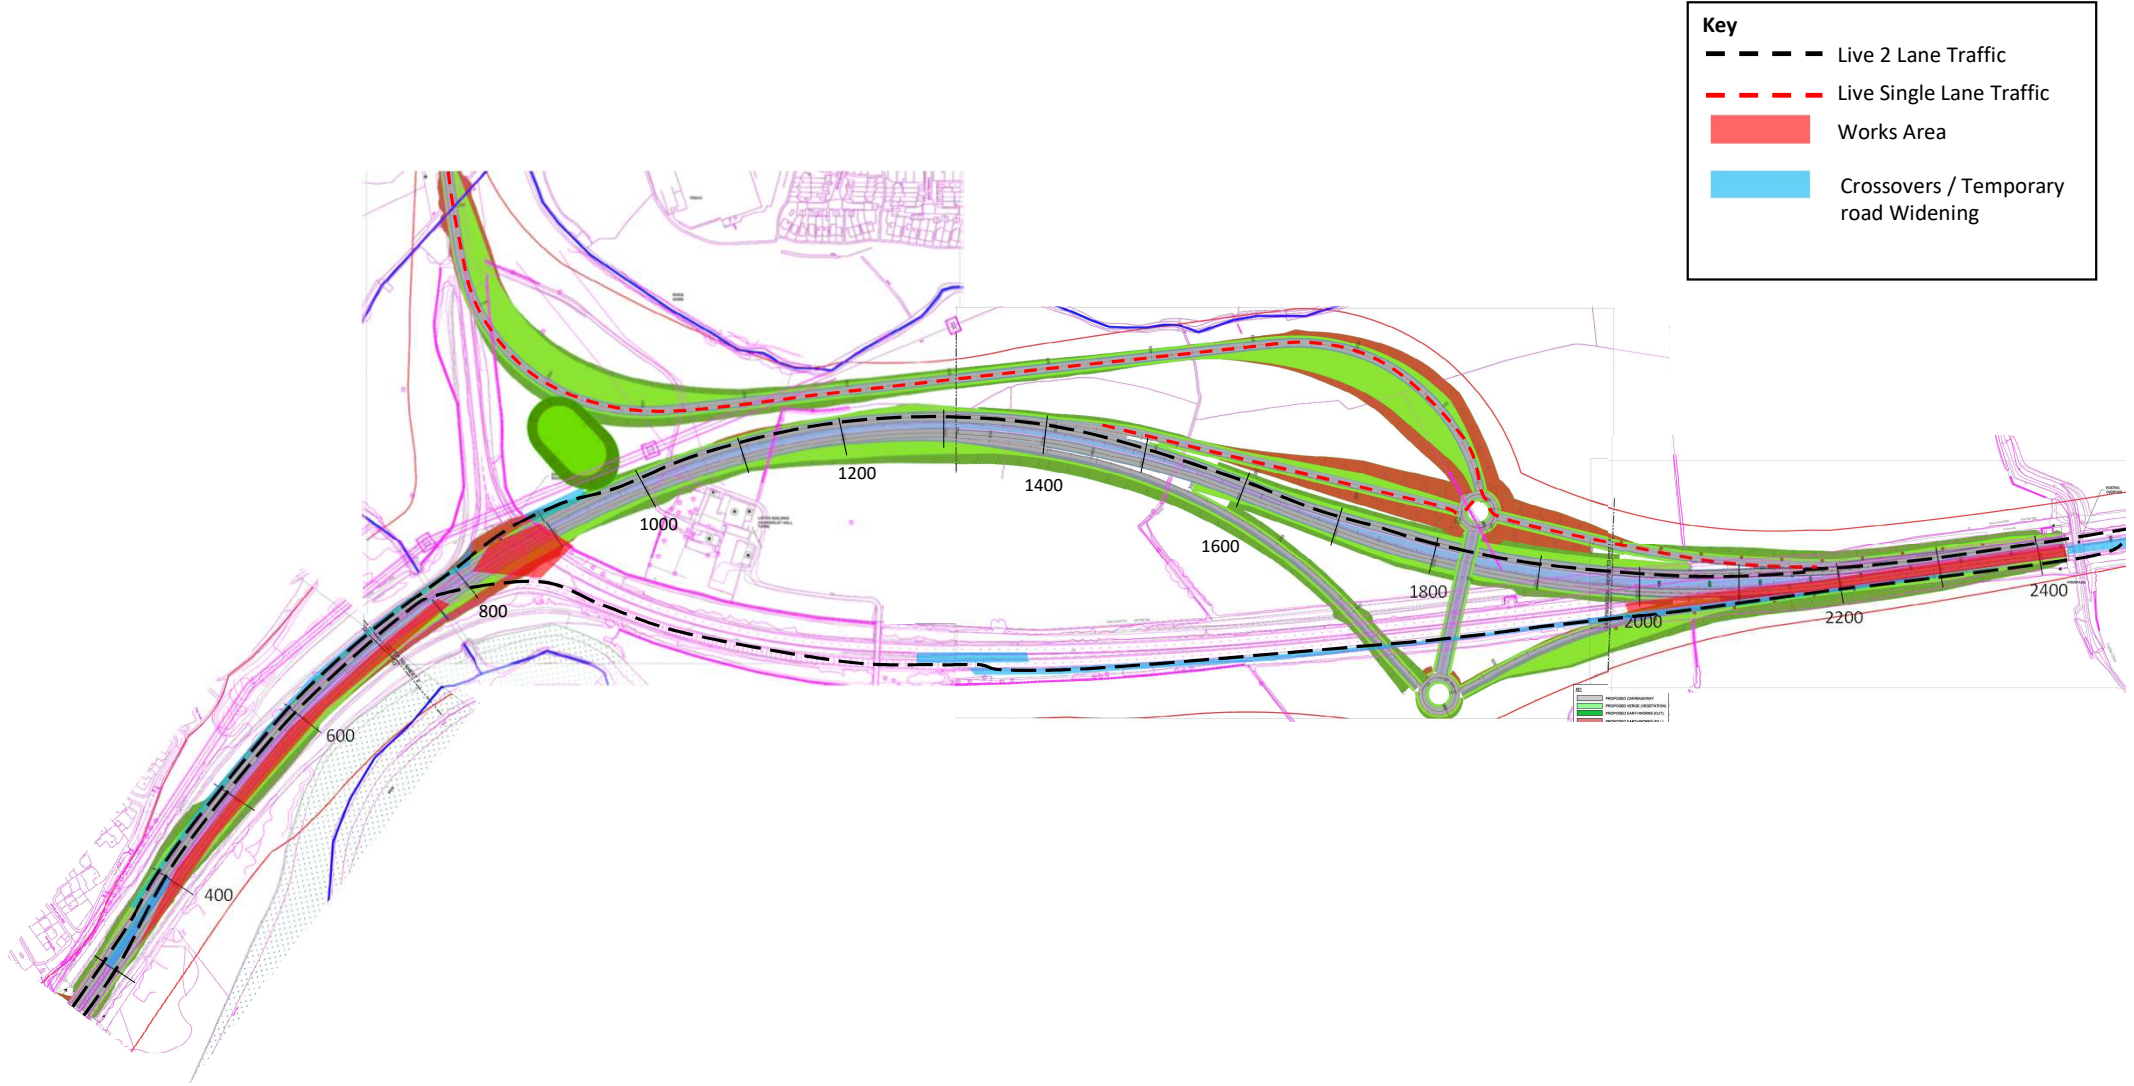


Option 6 – Phase 4

- All traffic on permanent alignment
- Completion of dumbbell roundabout works offline
- Overlay of remaining carriageway south of the roundabout – under weekend closures


Key

- Live 2 Lane Traffic
- - - Live Single Lane Traffic
- Works Area
- Crossovers / Temporary road Widening

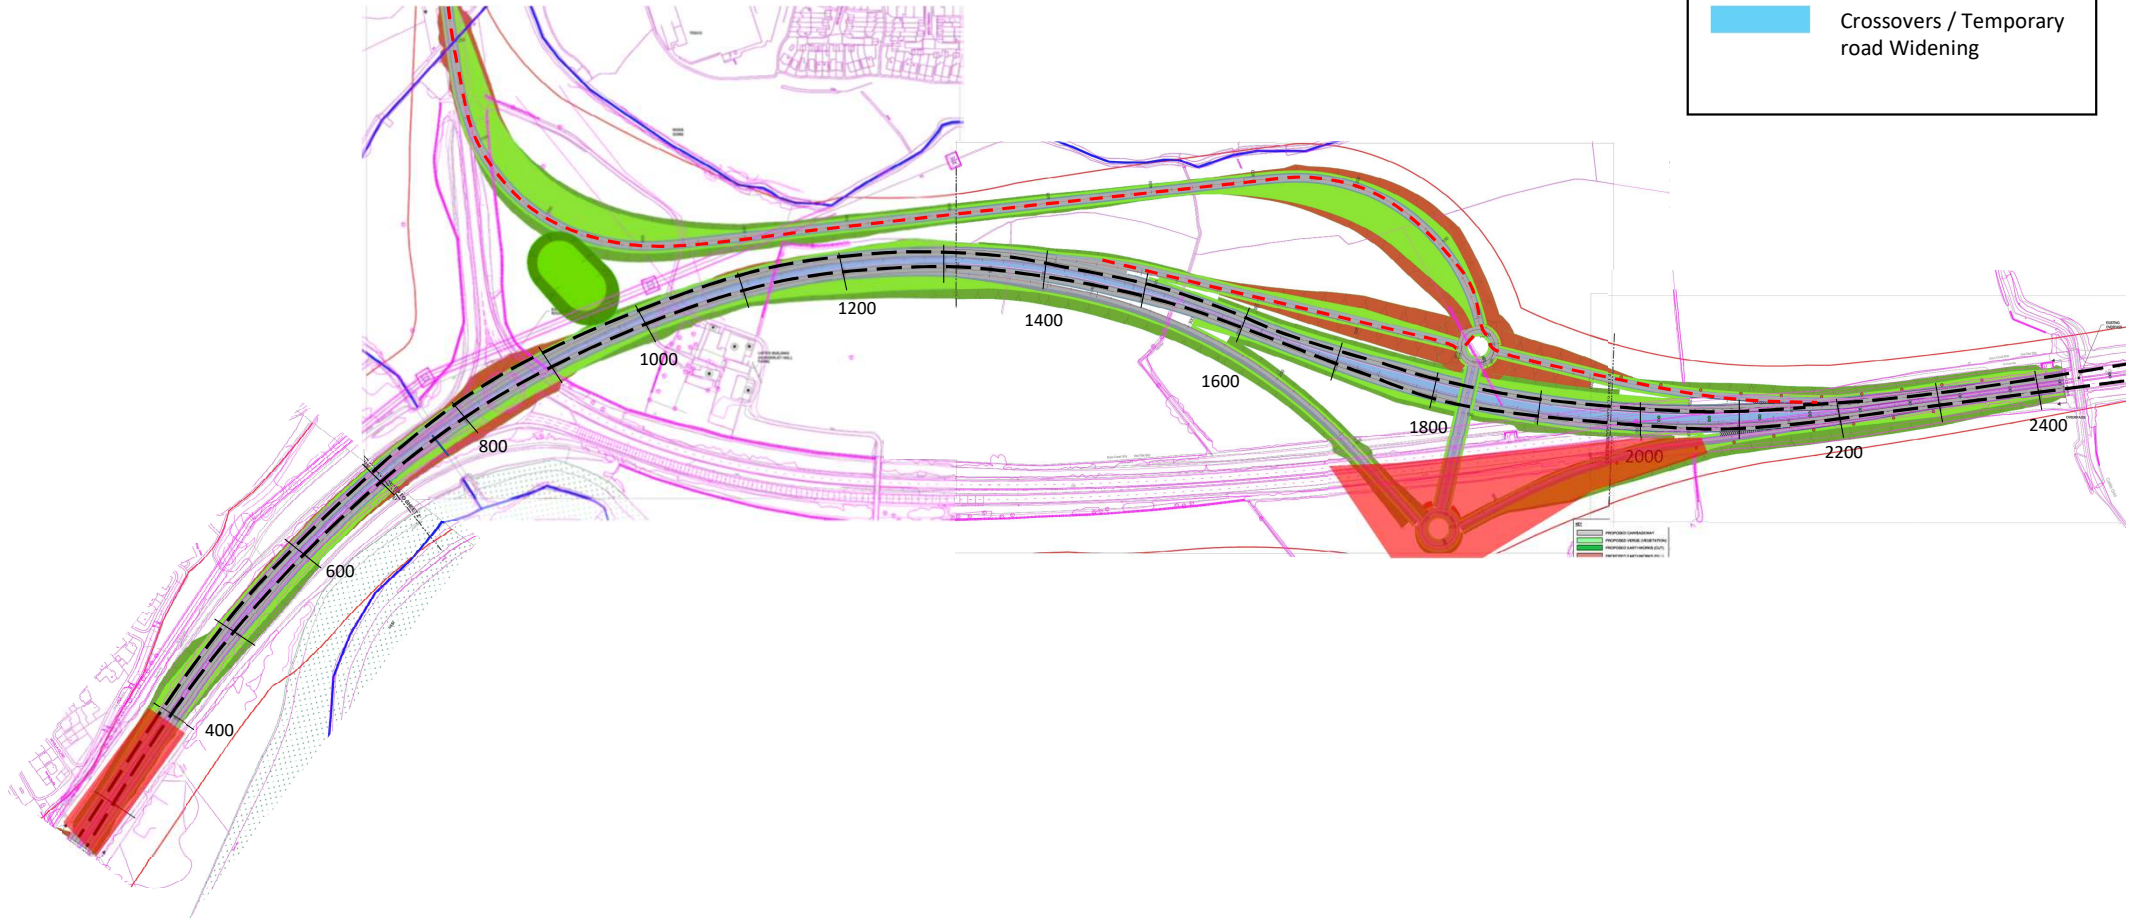


Option 7 – Phase 1

- Crossover installation & Temporary Carriageway Widening to NB Carriageway

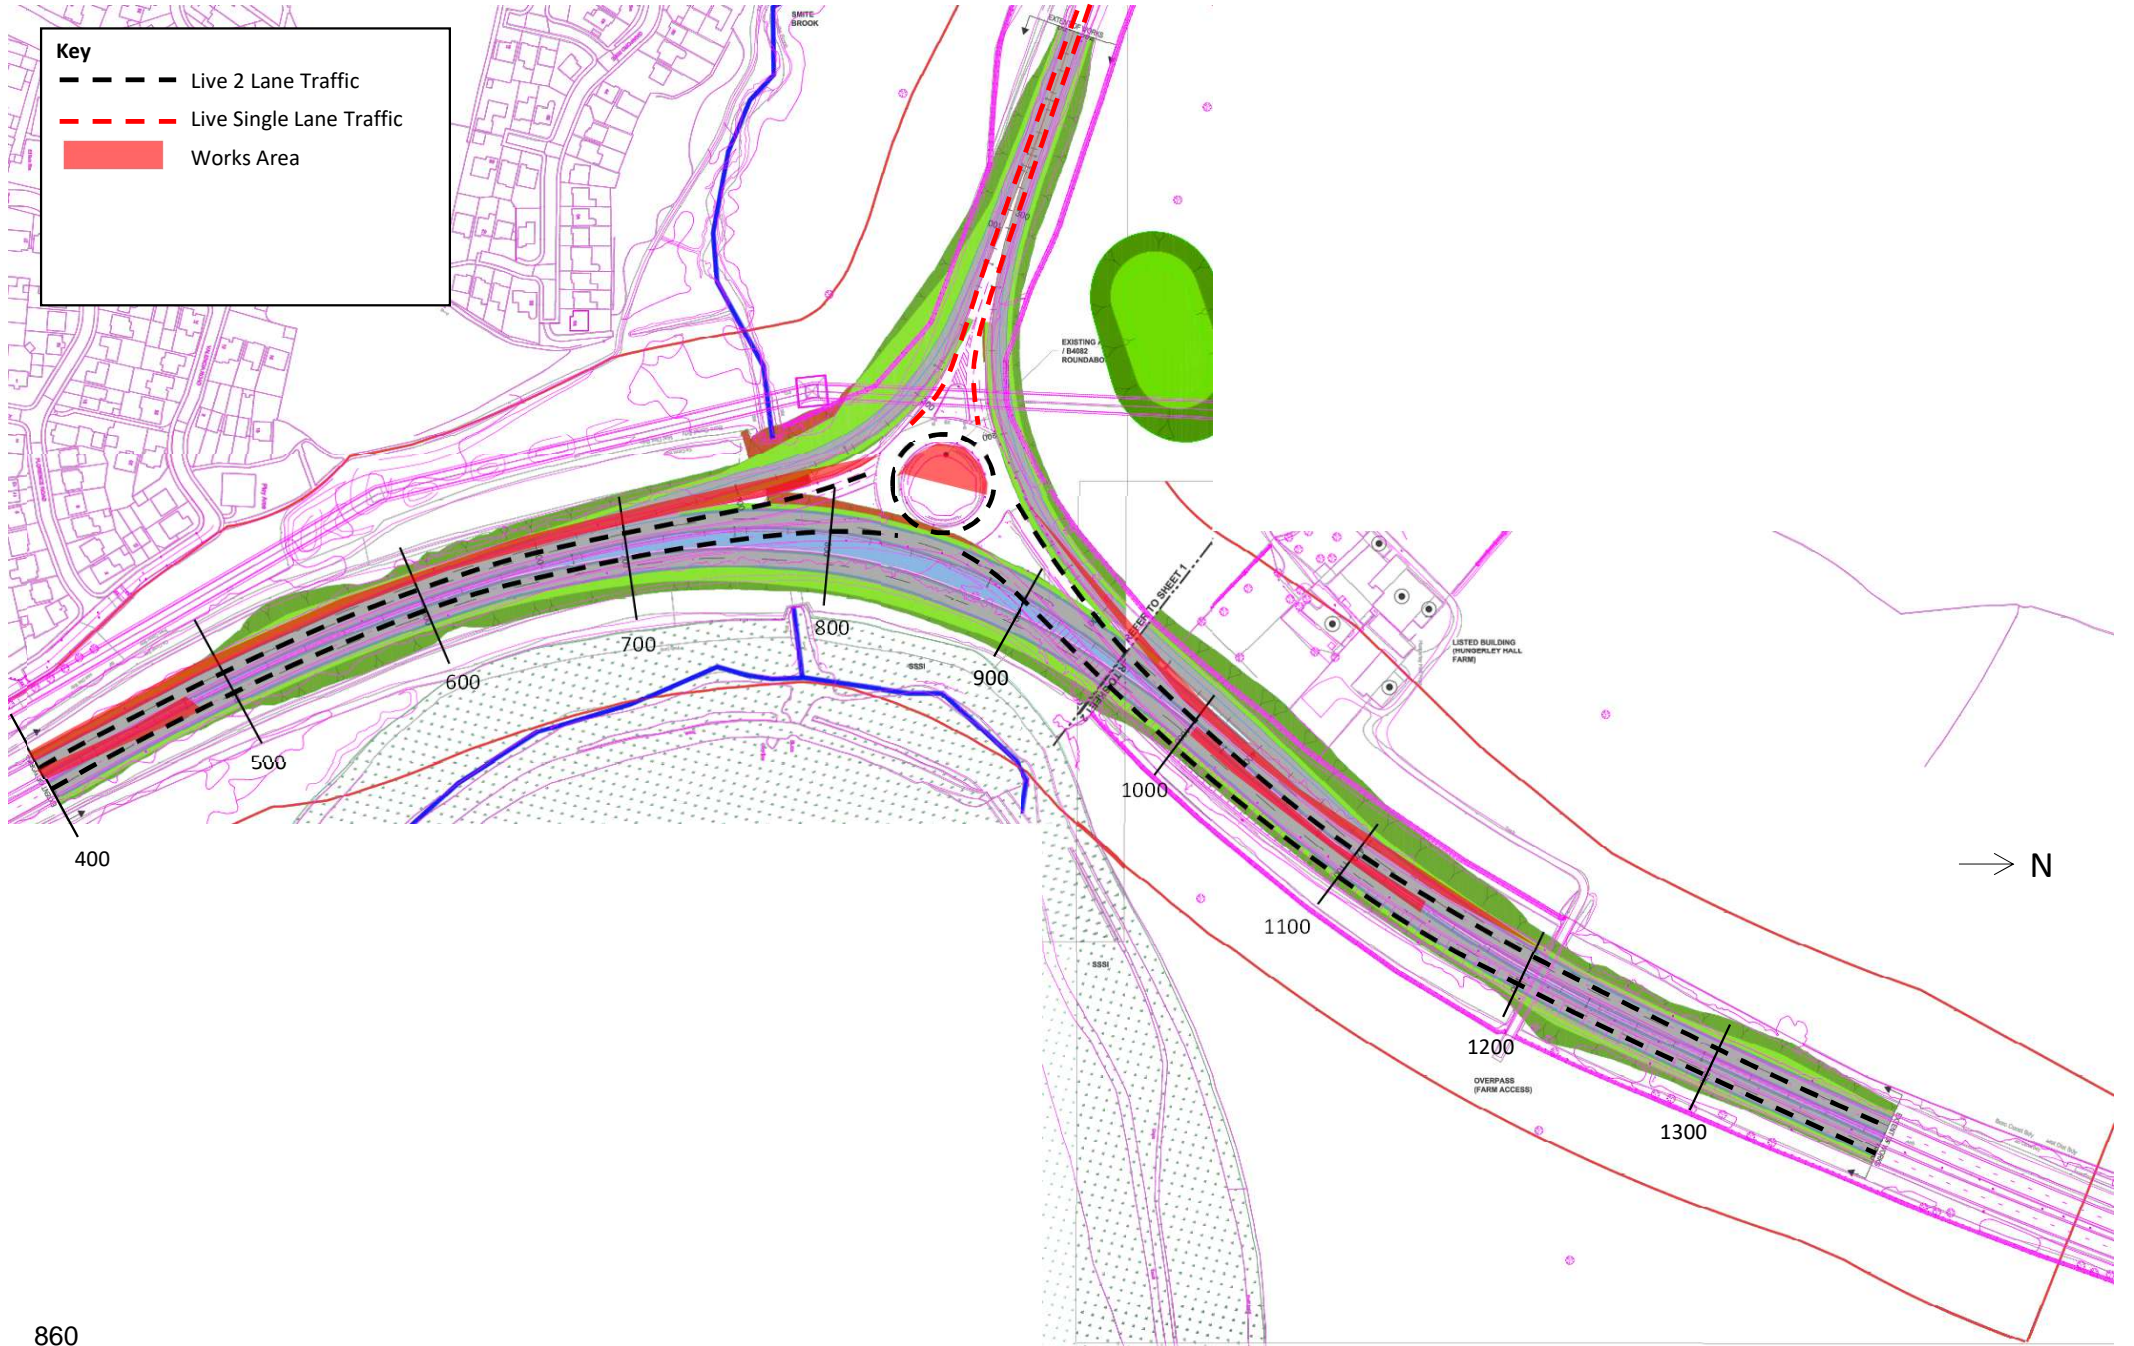

Option 7 – Phase 2

- Traffic running in dual contra flow on NB Carriageway .
- Construction of SB Carriageway including temporary widening for phase 3 works

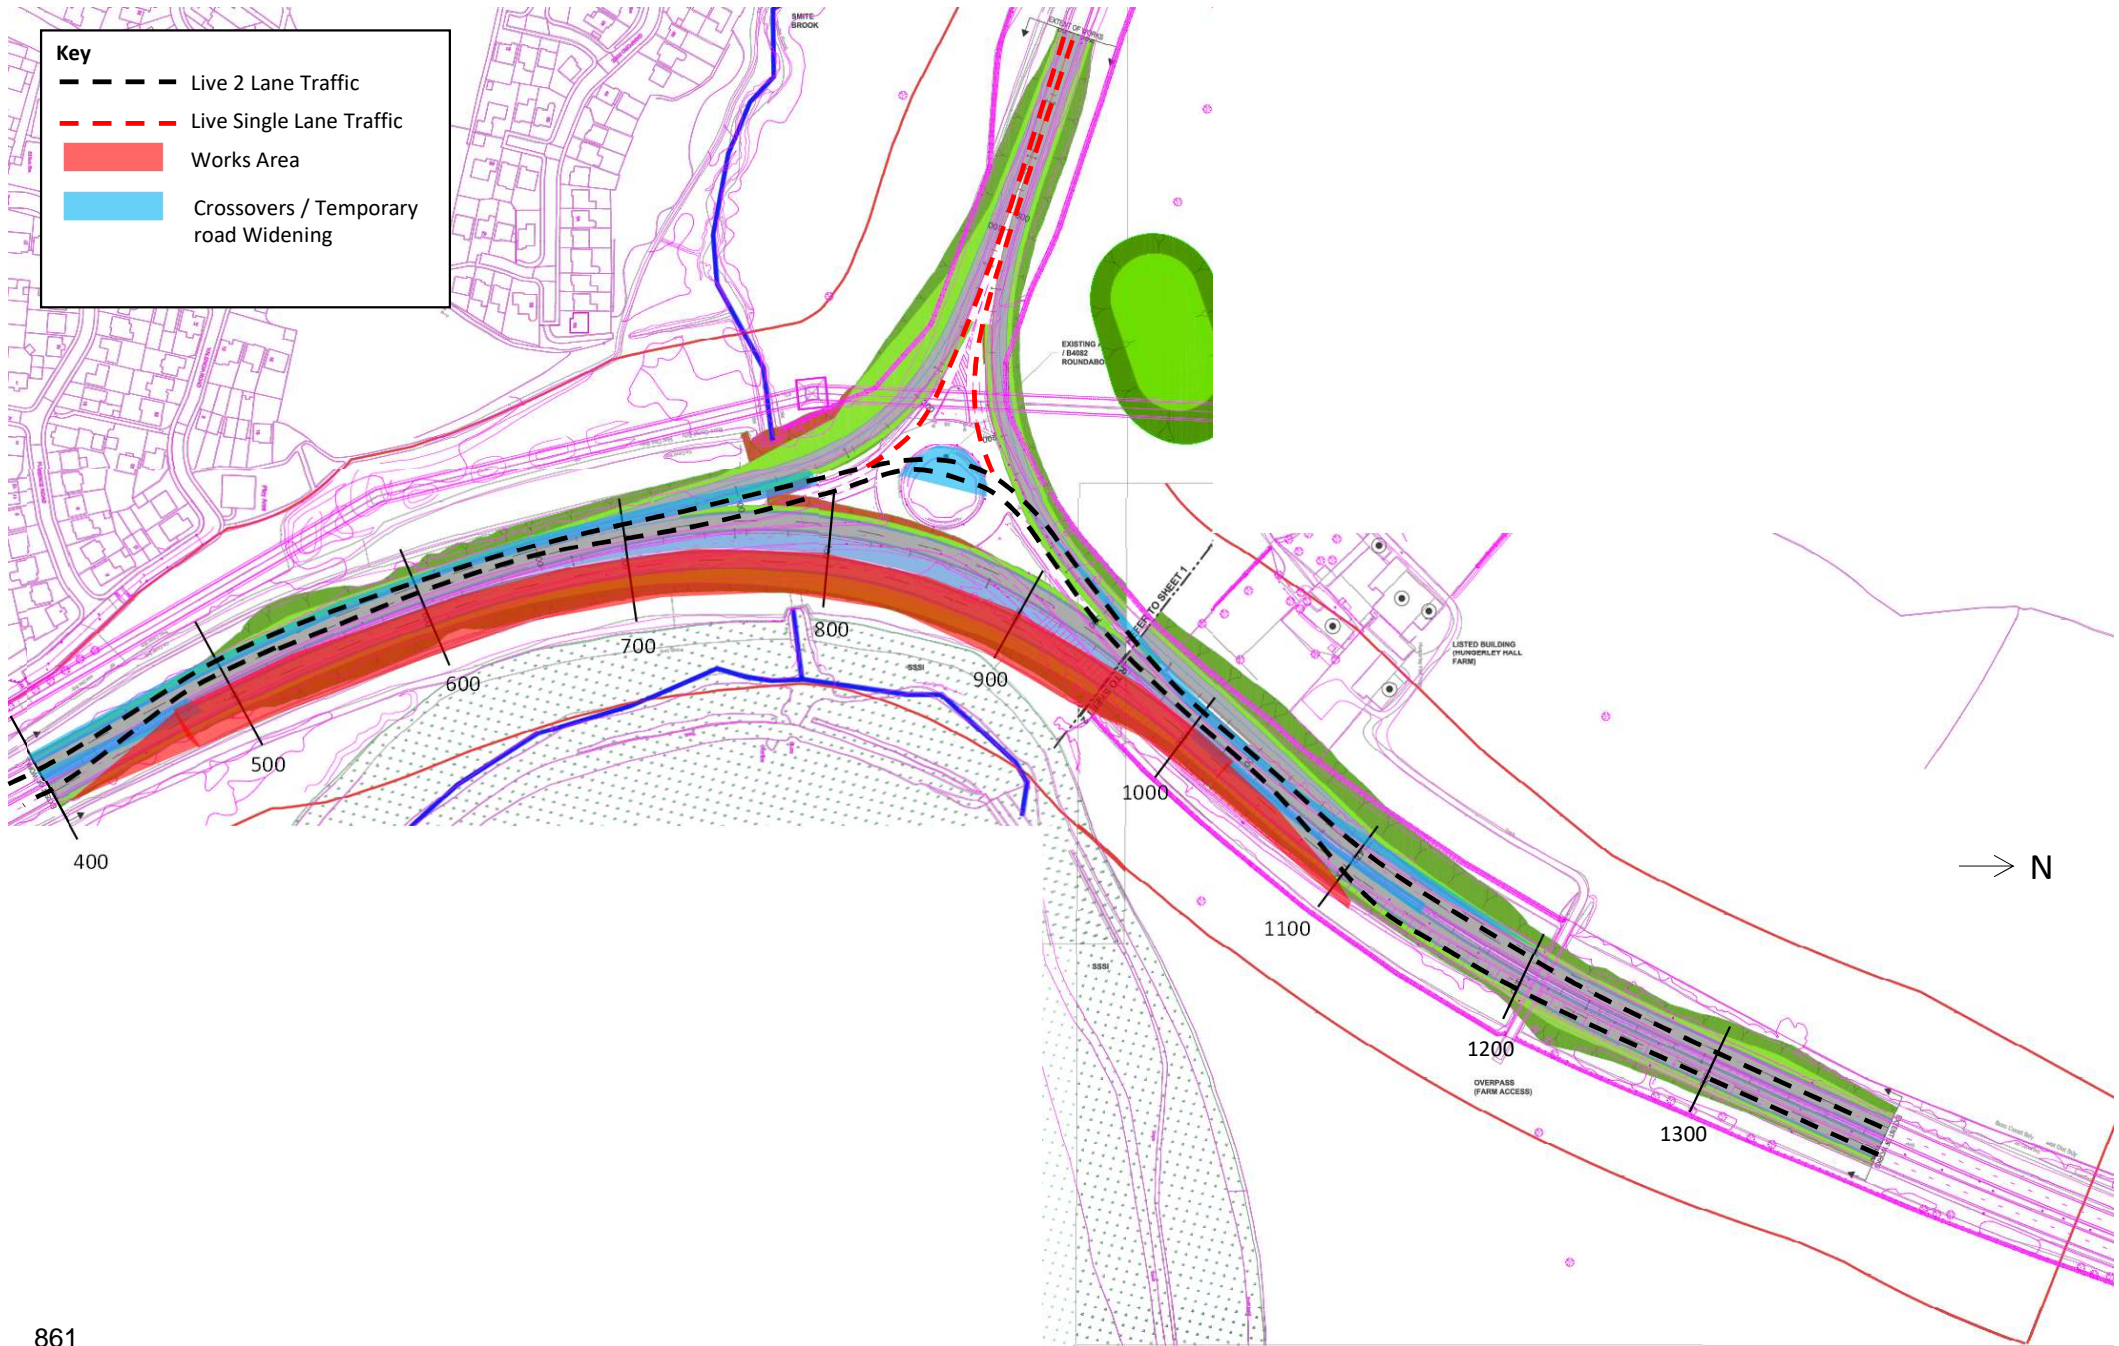

Option 7 – Phase 3


- Traffic running in dual contra flow on SB Carriageway .
- Construction of NB Carriageway & local road works






Option 8 – Phase 1

- Crossover installation & Temporary Carriageway Widening to SB Carriageway

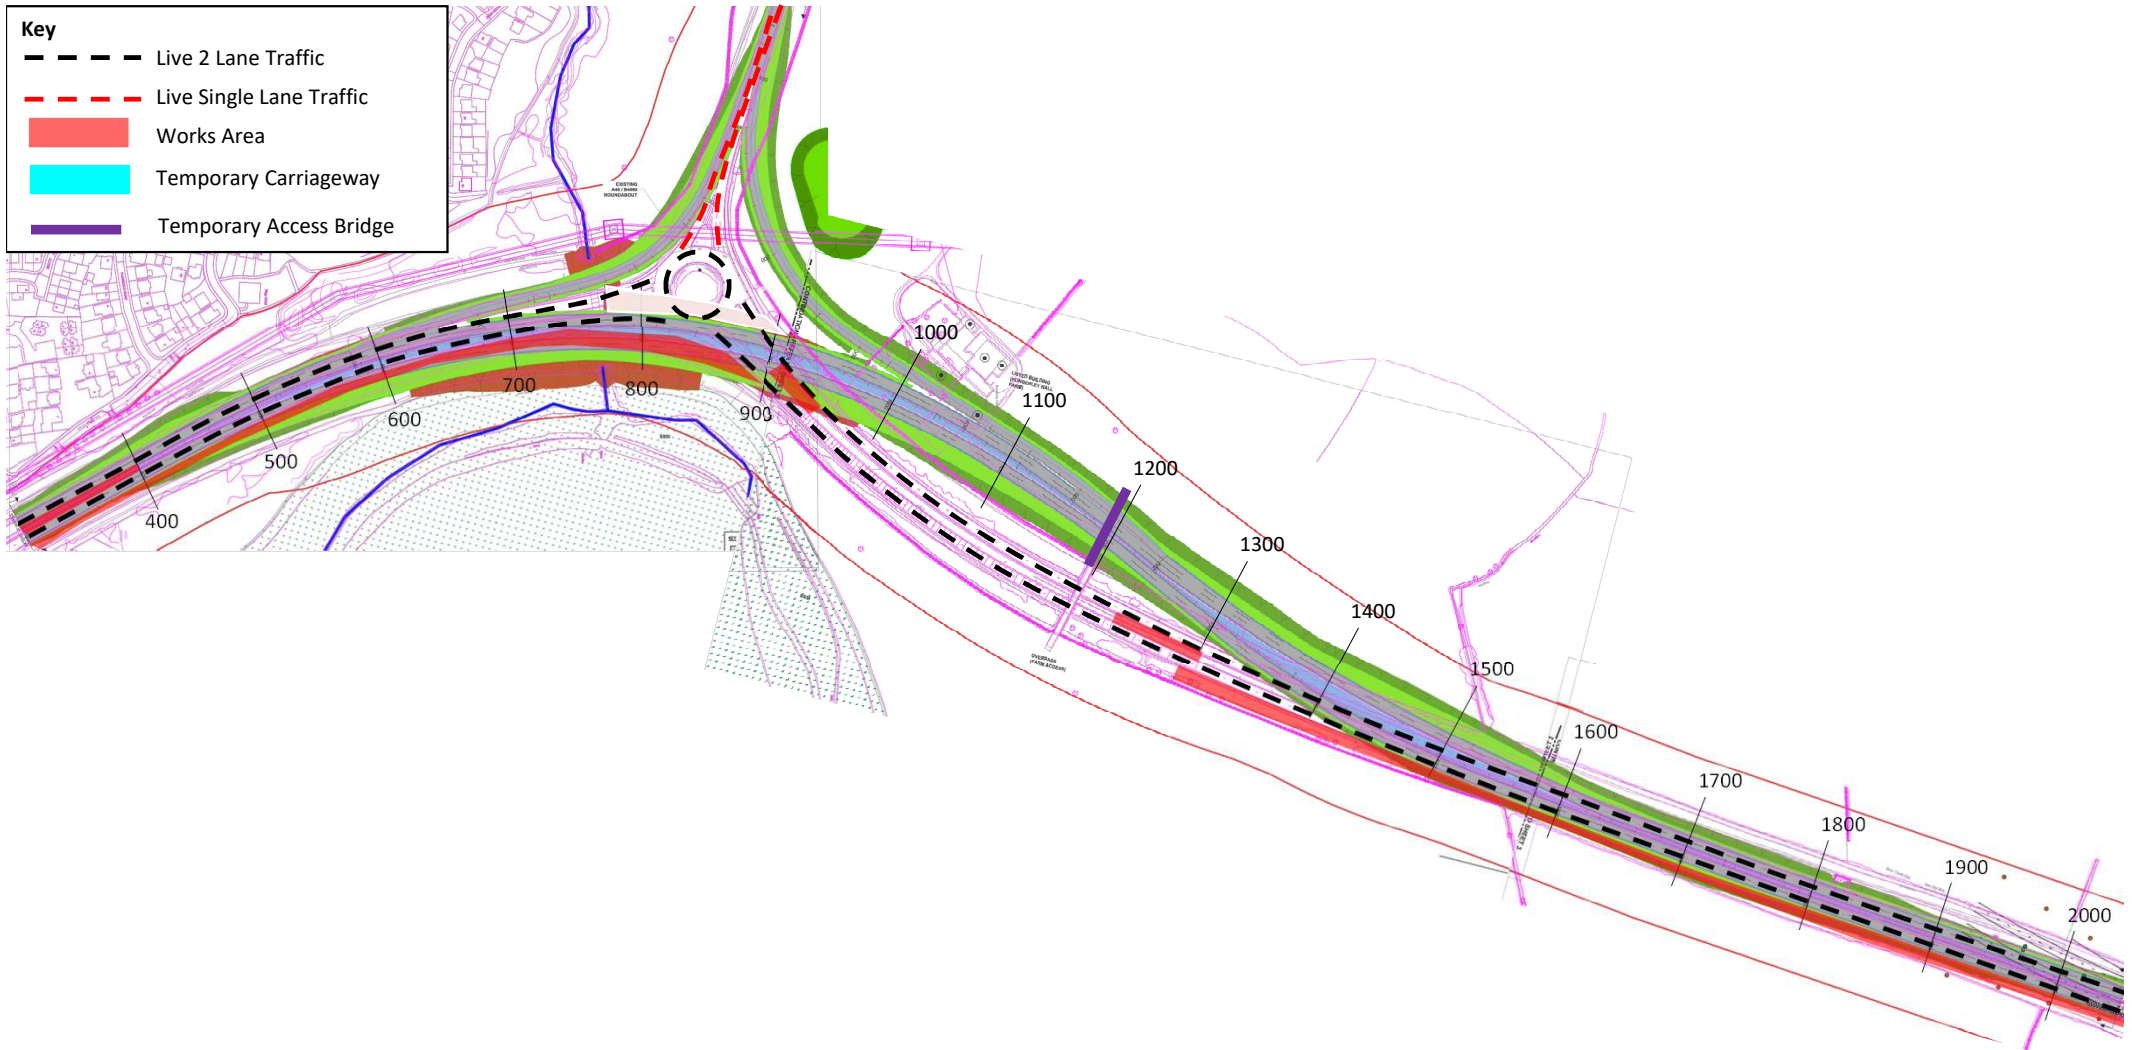


Option 8 – Phase 2

- Construction of offline works
- Traffic in Dual Contraflow on Sb Carriageway

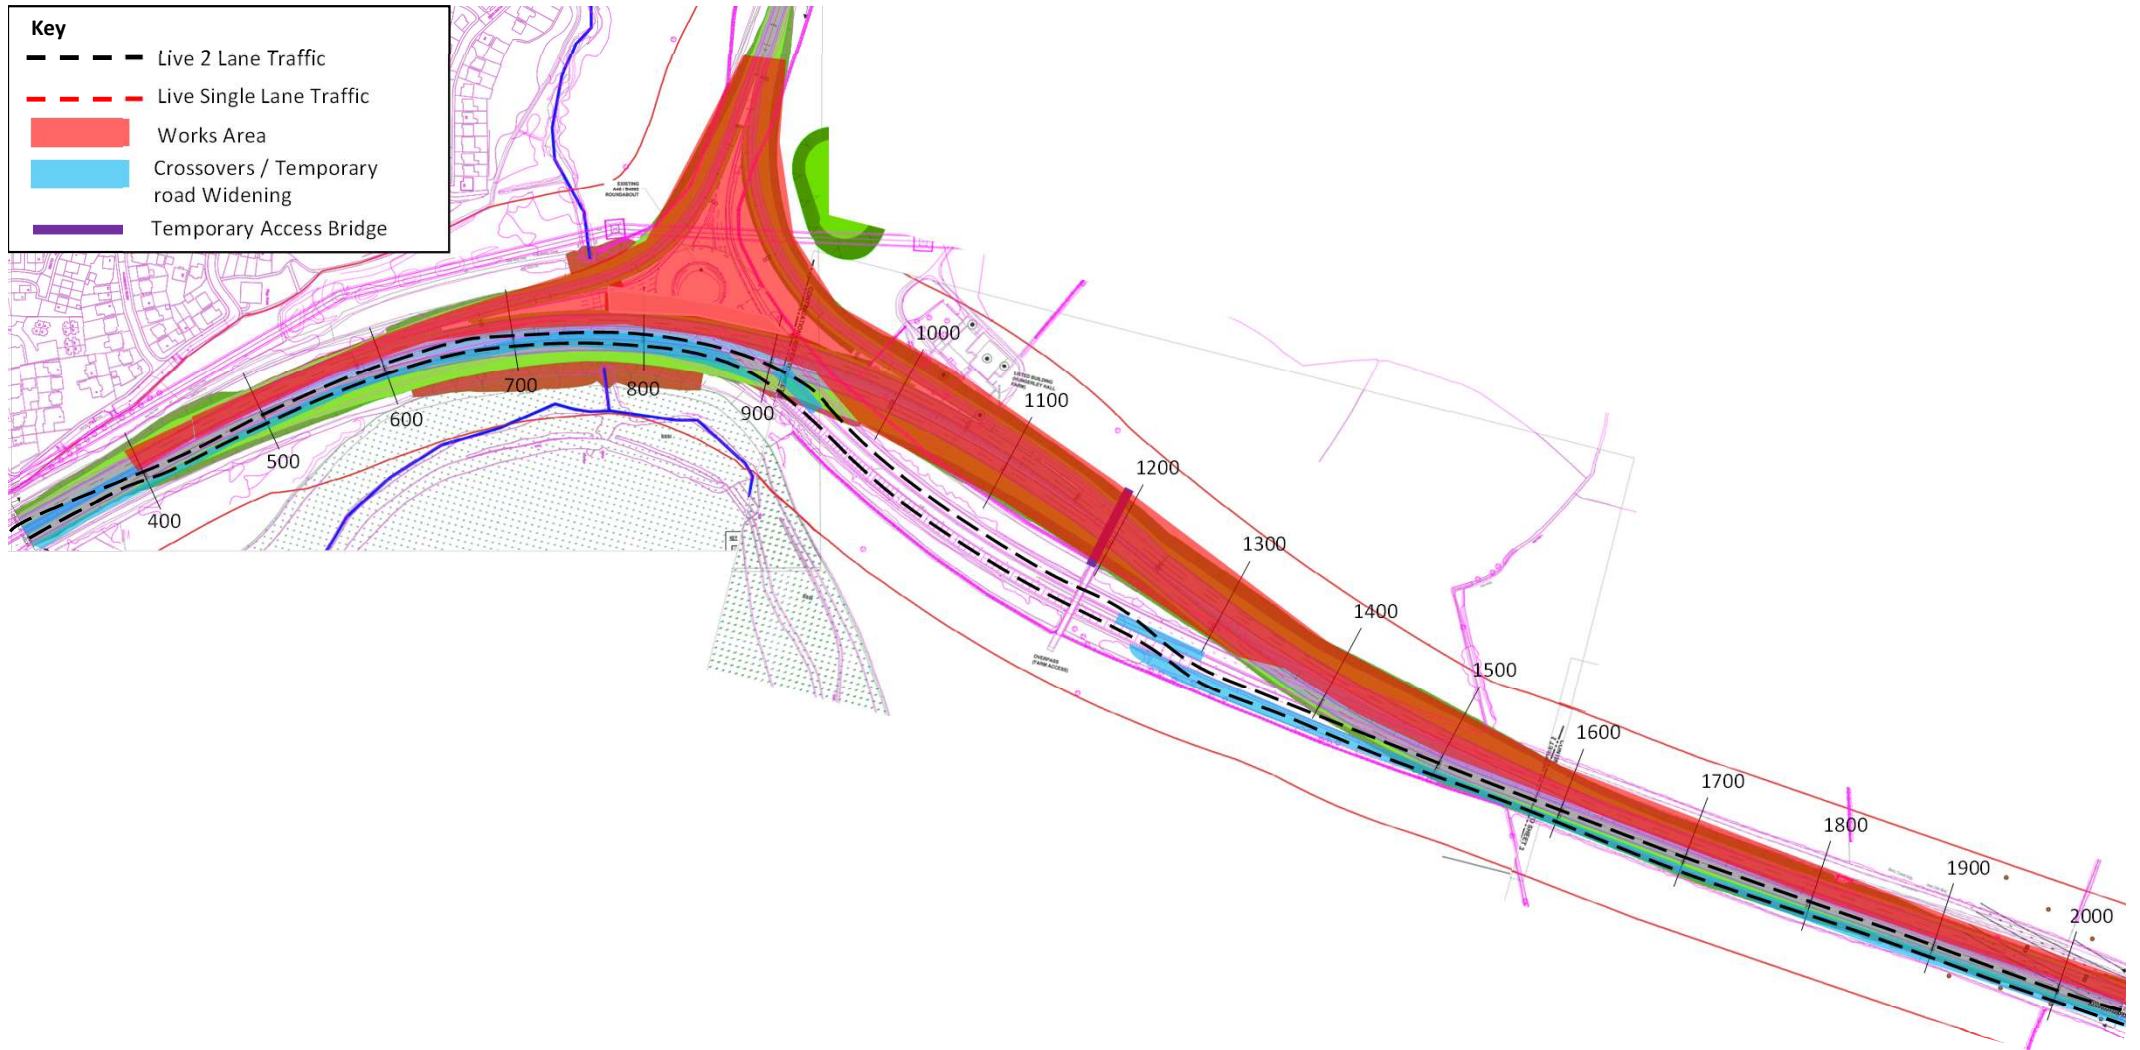


Option 8 – Phase 3

- Traffic on proposed NB alignment and SB temporary widening / existing
- Completion of SB carriageway

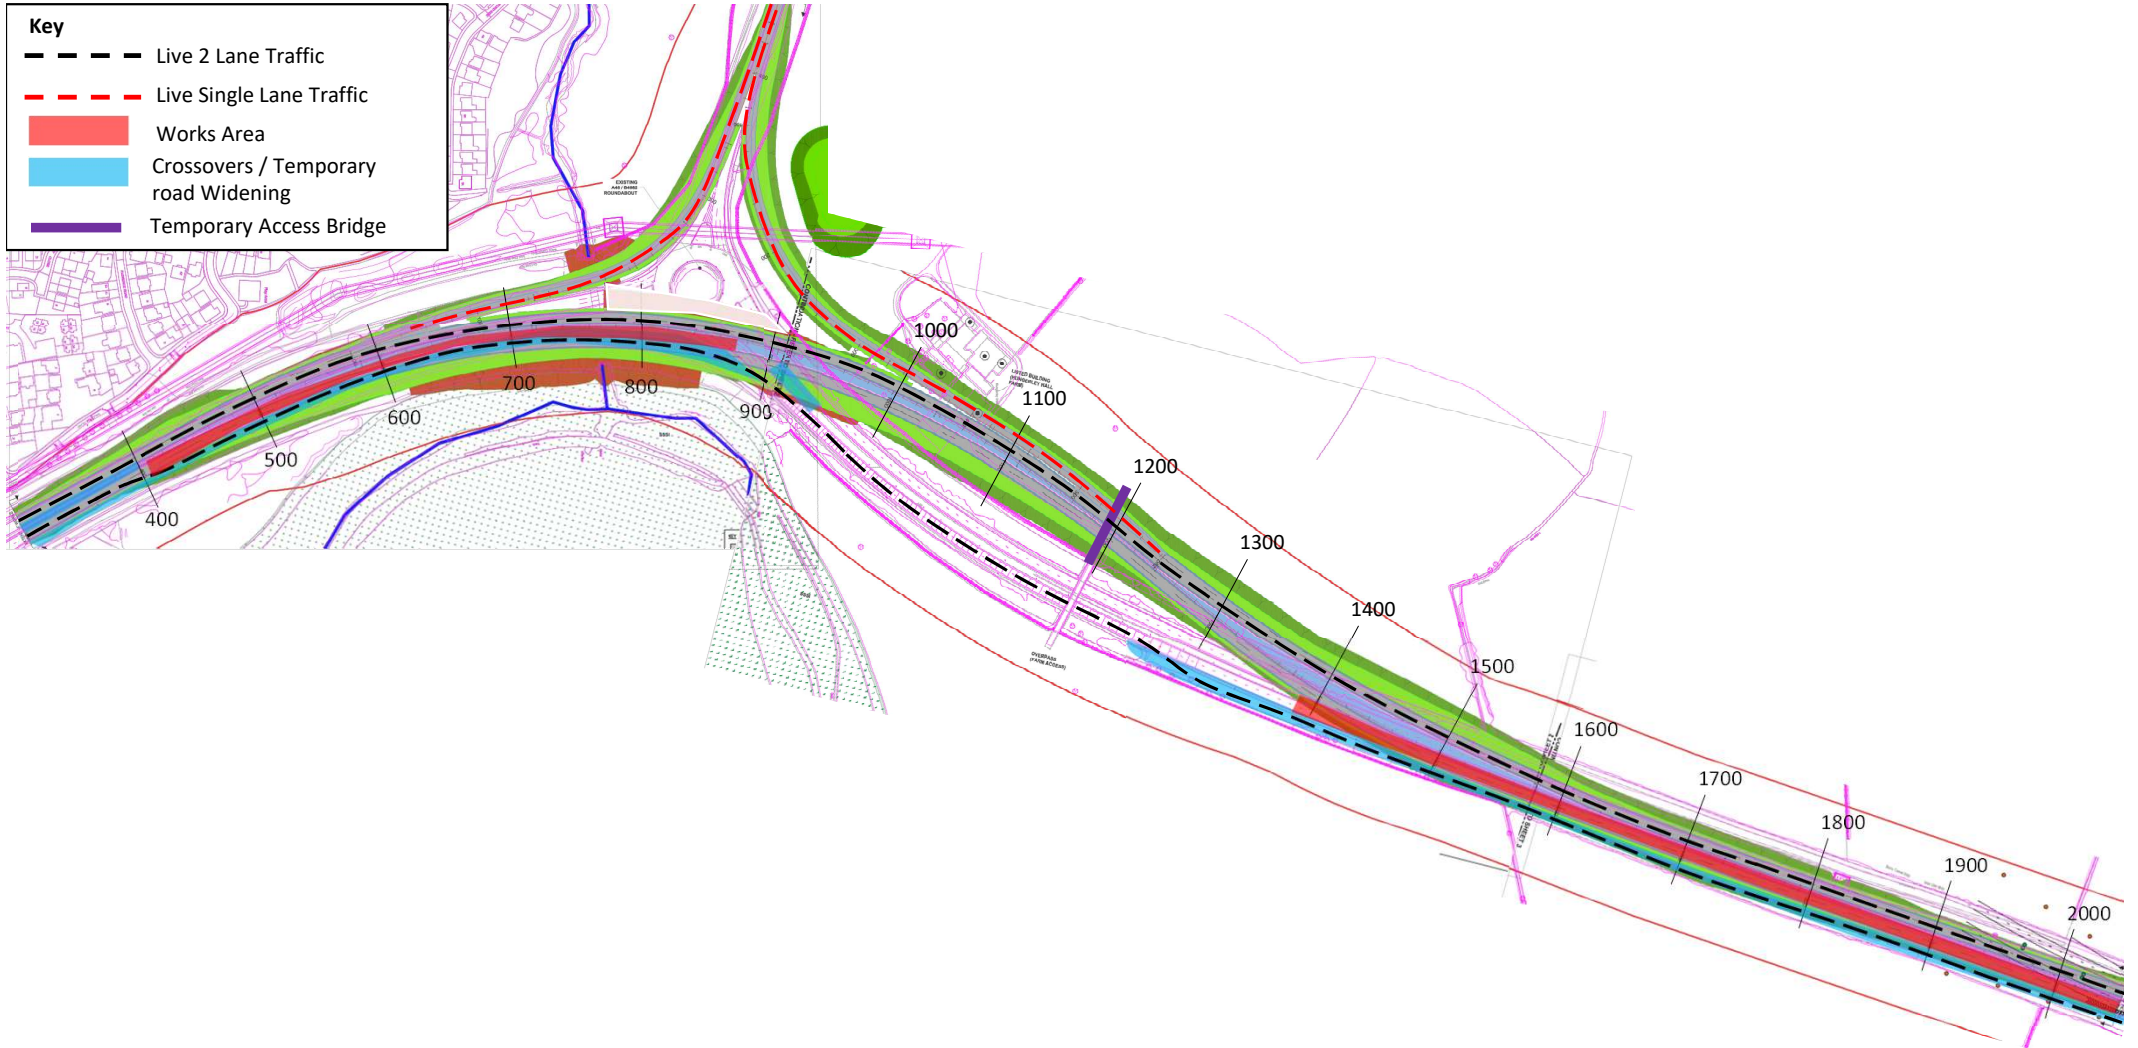

Option 8 – Phase 4


- All traffic on permanent alignment
- Overlay of remaining carriageway south of the roundabout – under weekend closures

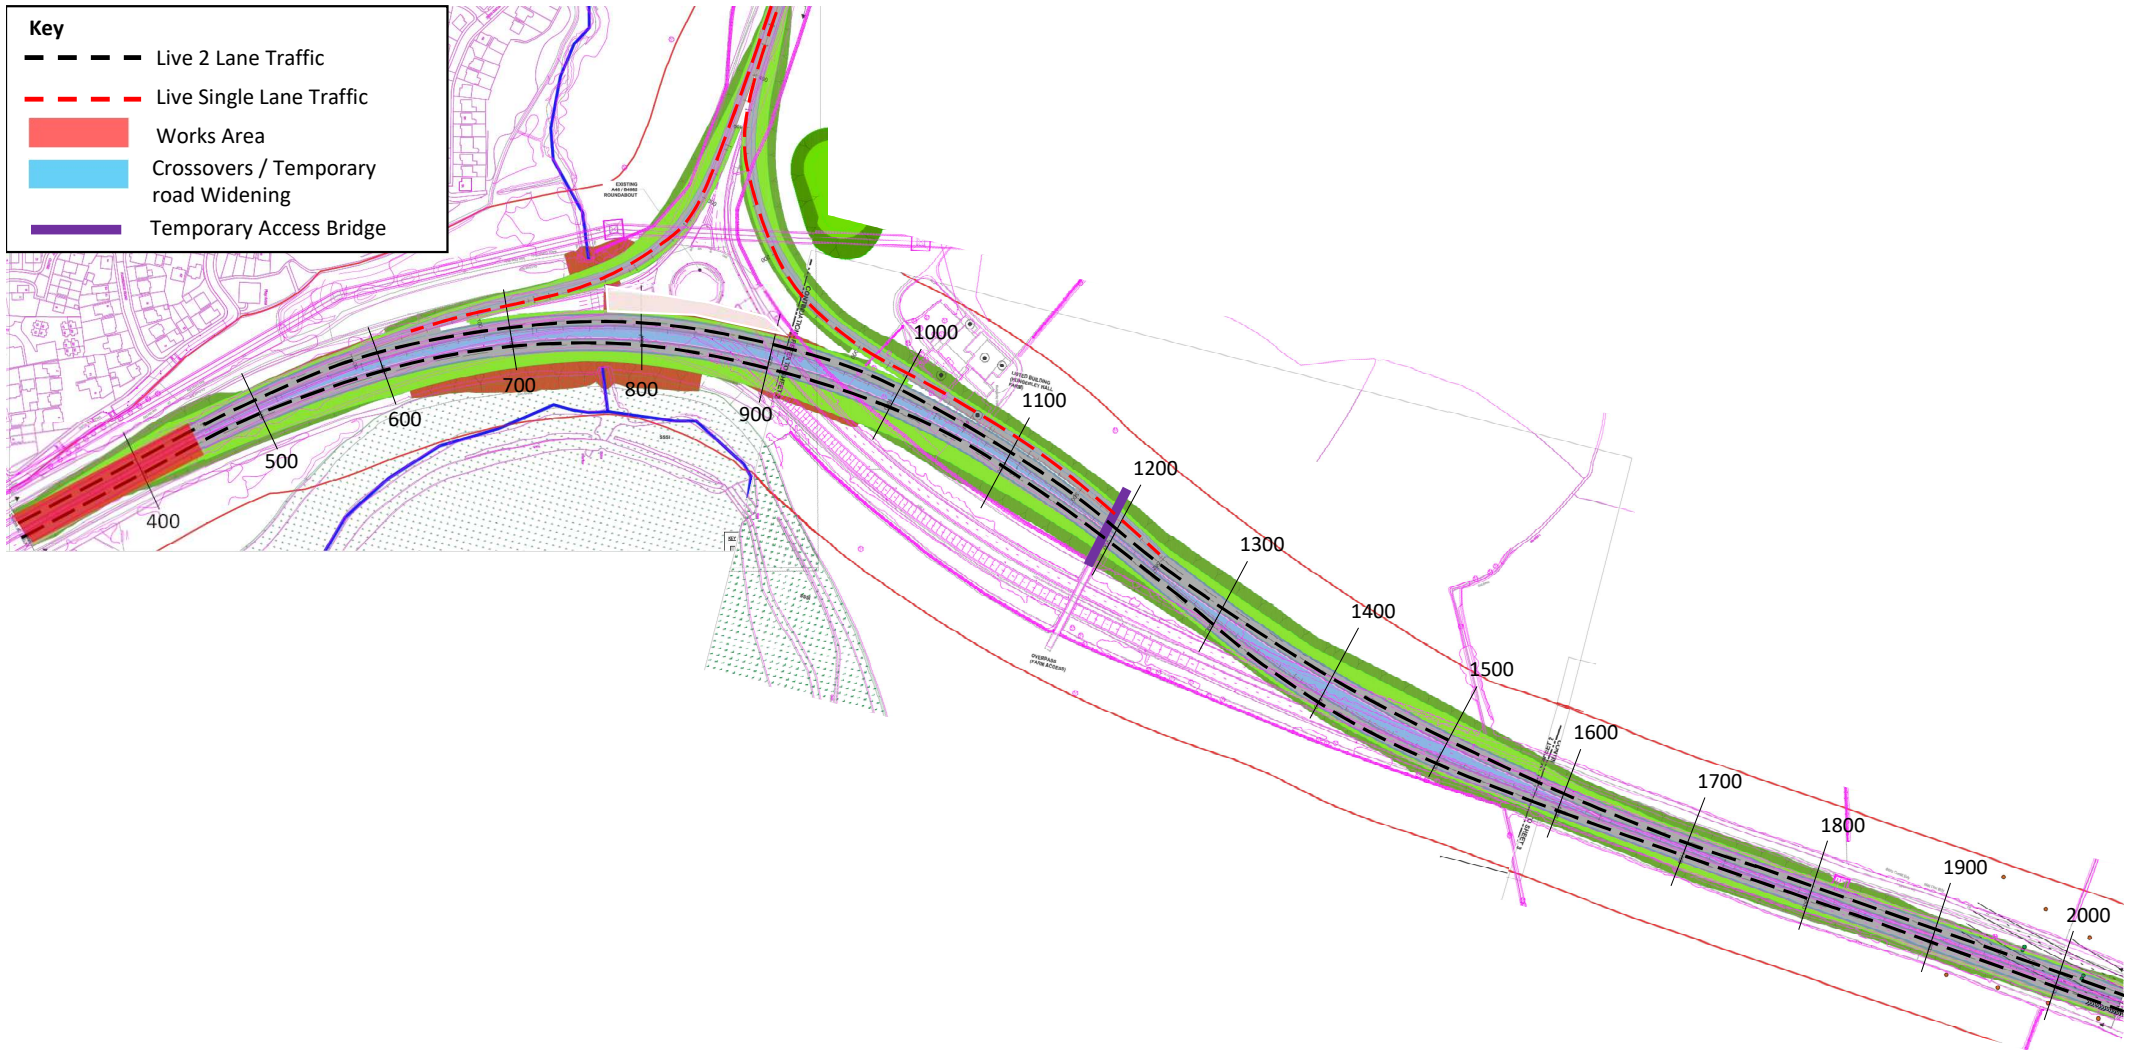




A

Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:	
	Drawing Title:	Option 11 Phase 1 - A		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>			
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear		Date:	17/08/21	HAZARD/RISK	
	Revision details			Verified by:			Date:			HIGH/MED/LOW
	Revision	-	Sheet No. 2 of 5	Validation by:			Date:			
	Revised by:	Rev:	Date:	Original size	A1	Scale	NTS			
				Technical Support						
				Designer Checklist No:	xxx					
				Technical Note & Design Commentary No:	xxx					
				Associated Risk Assessment No:	xxx					
				Layer Register No:	xxx					
				DWG File Number No:	xxx					

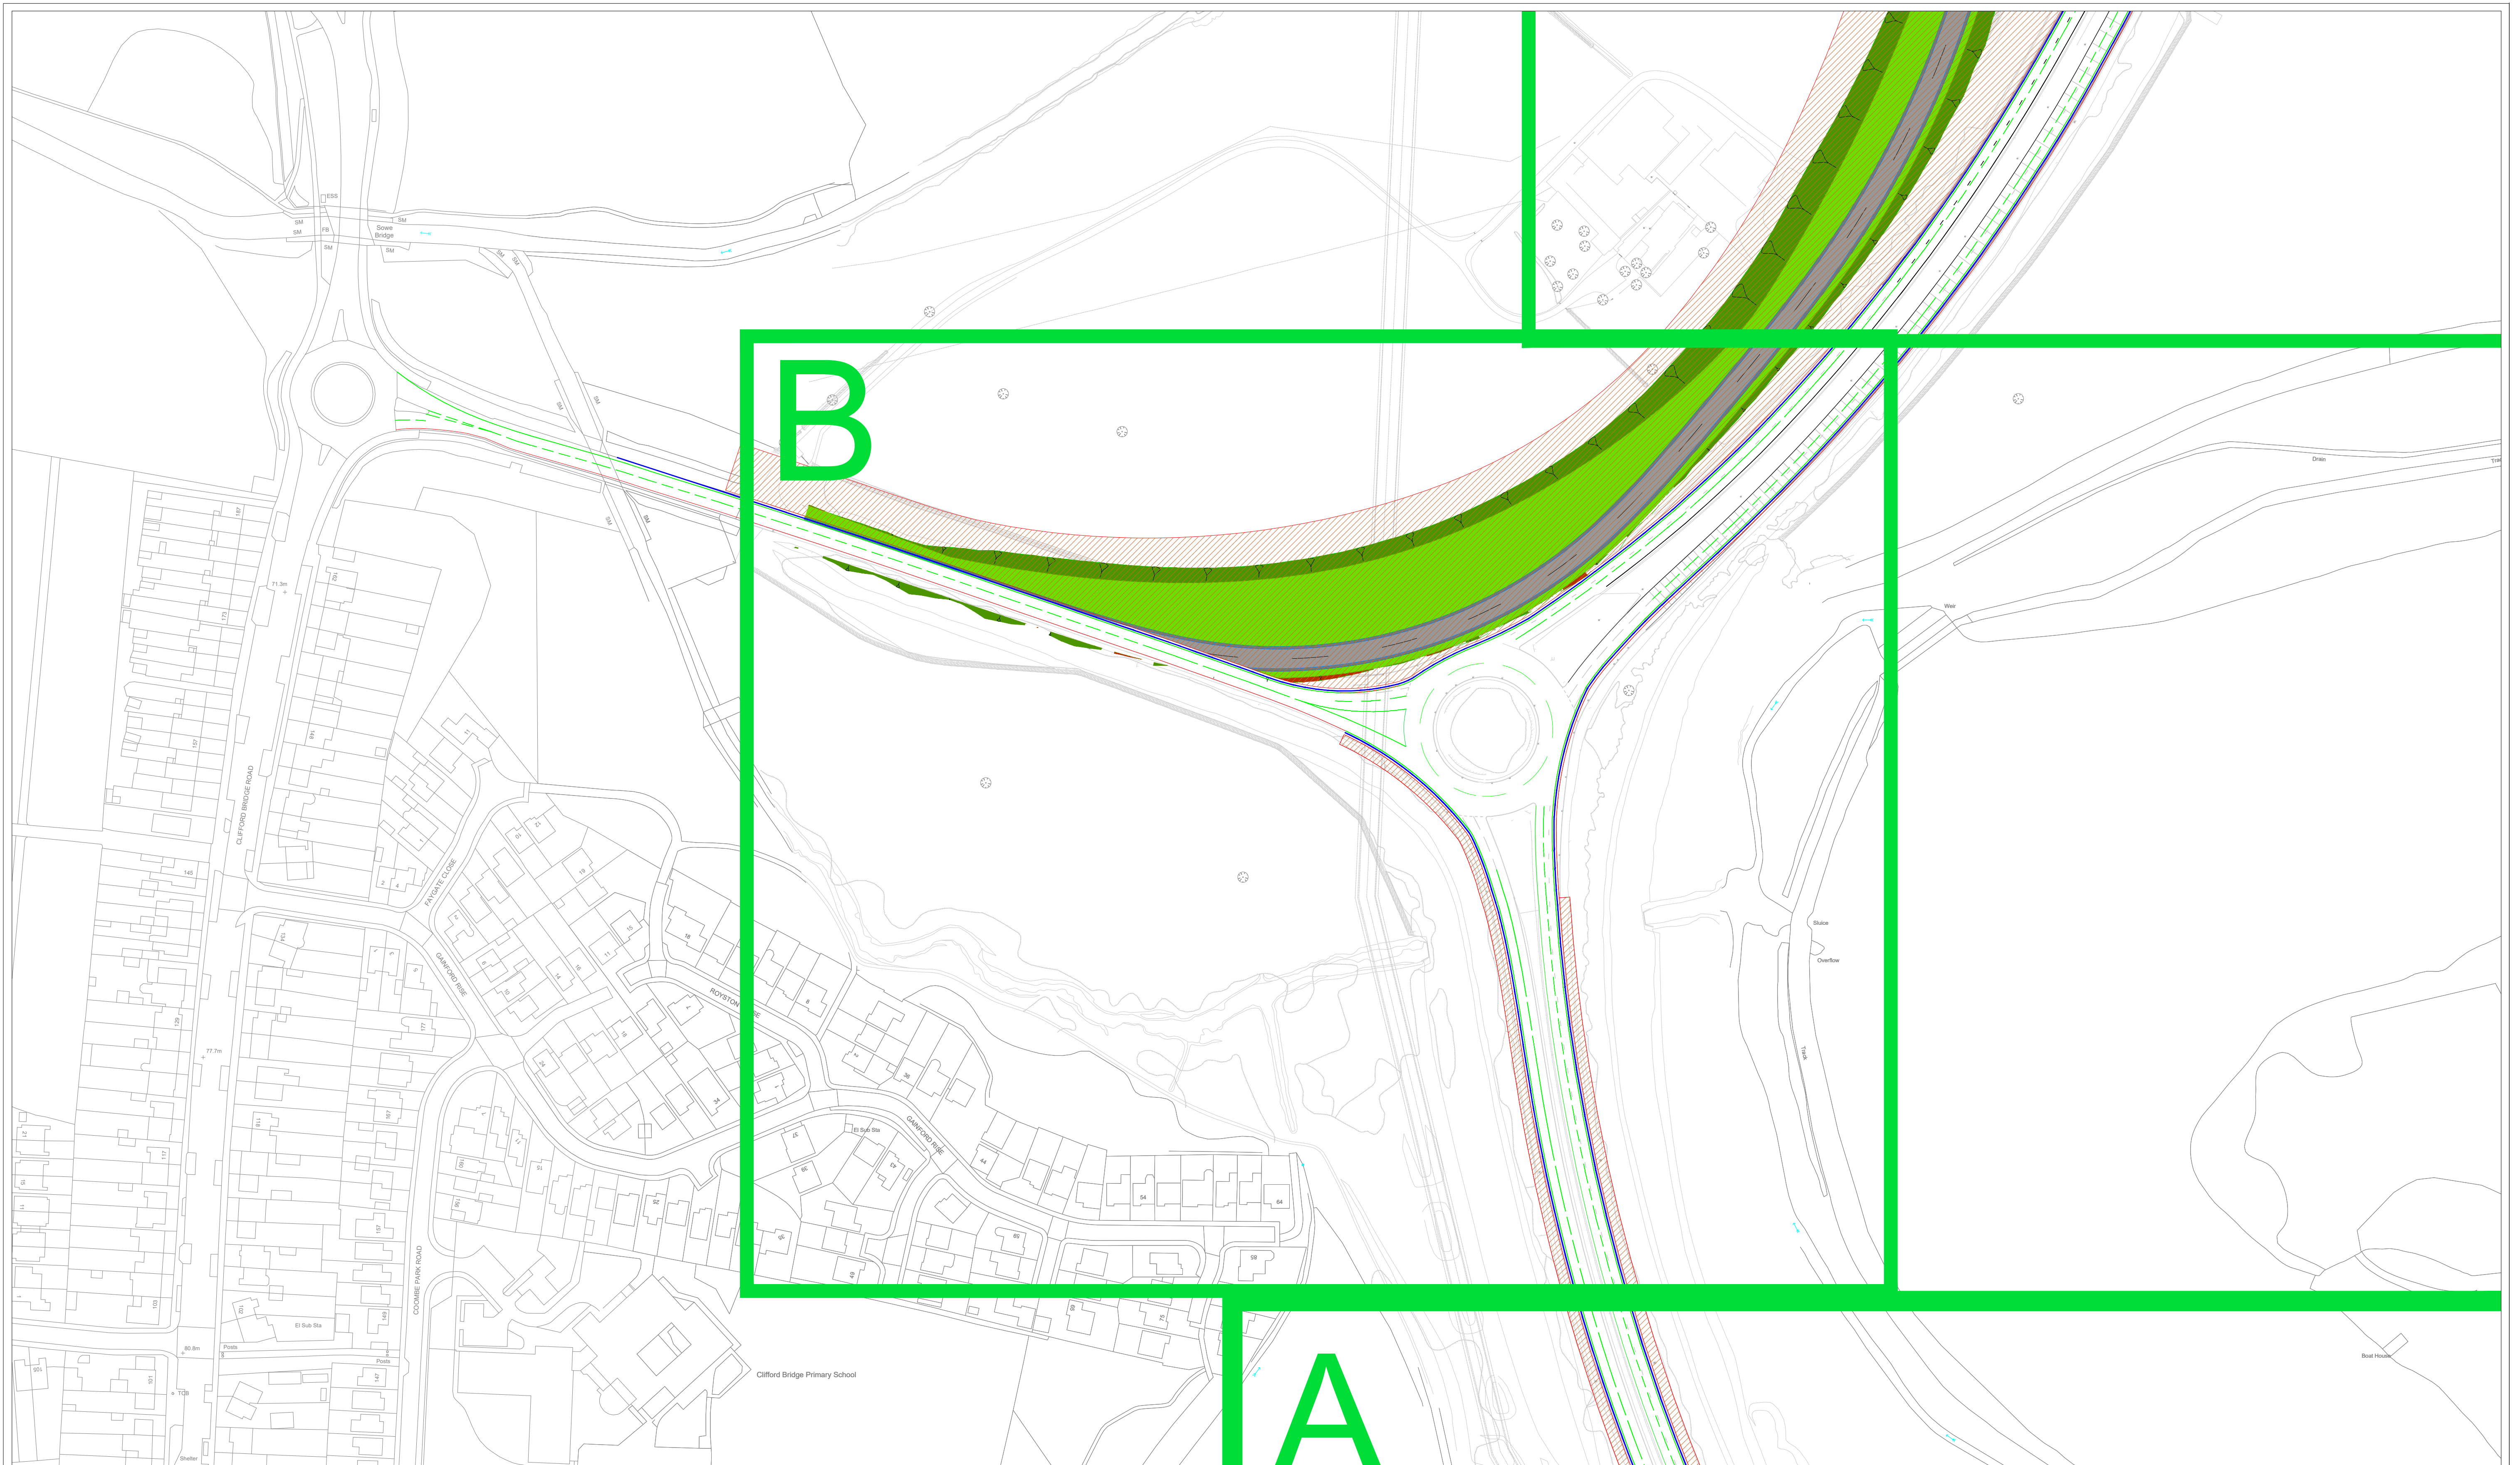


Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title:	Option 11 Phase 1 - B		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>		
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear	Date:	17/08/21	HAZARD/RISK	HIGH/MED/LOW
	Revision details	Revision Sheet No. 3 of 5		Verified by:		Date:			
				Validation by:		Date:		1	
				Original size	A1	Scale	NTS		
				Technical Support					
				Designer Checklist No.:	xxx				
				Technical Note & Design Commentary No.:	xxx				
				Associated Risk Assessment No.:	xxx				
				Layer Register No.:	xxx				
				DWG File Number No.:	xxx				

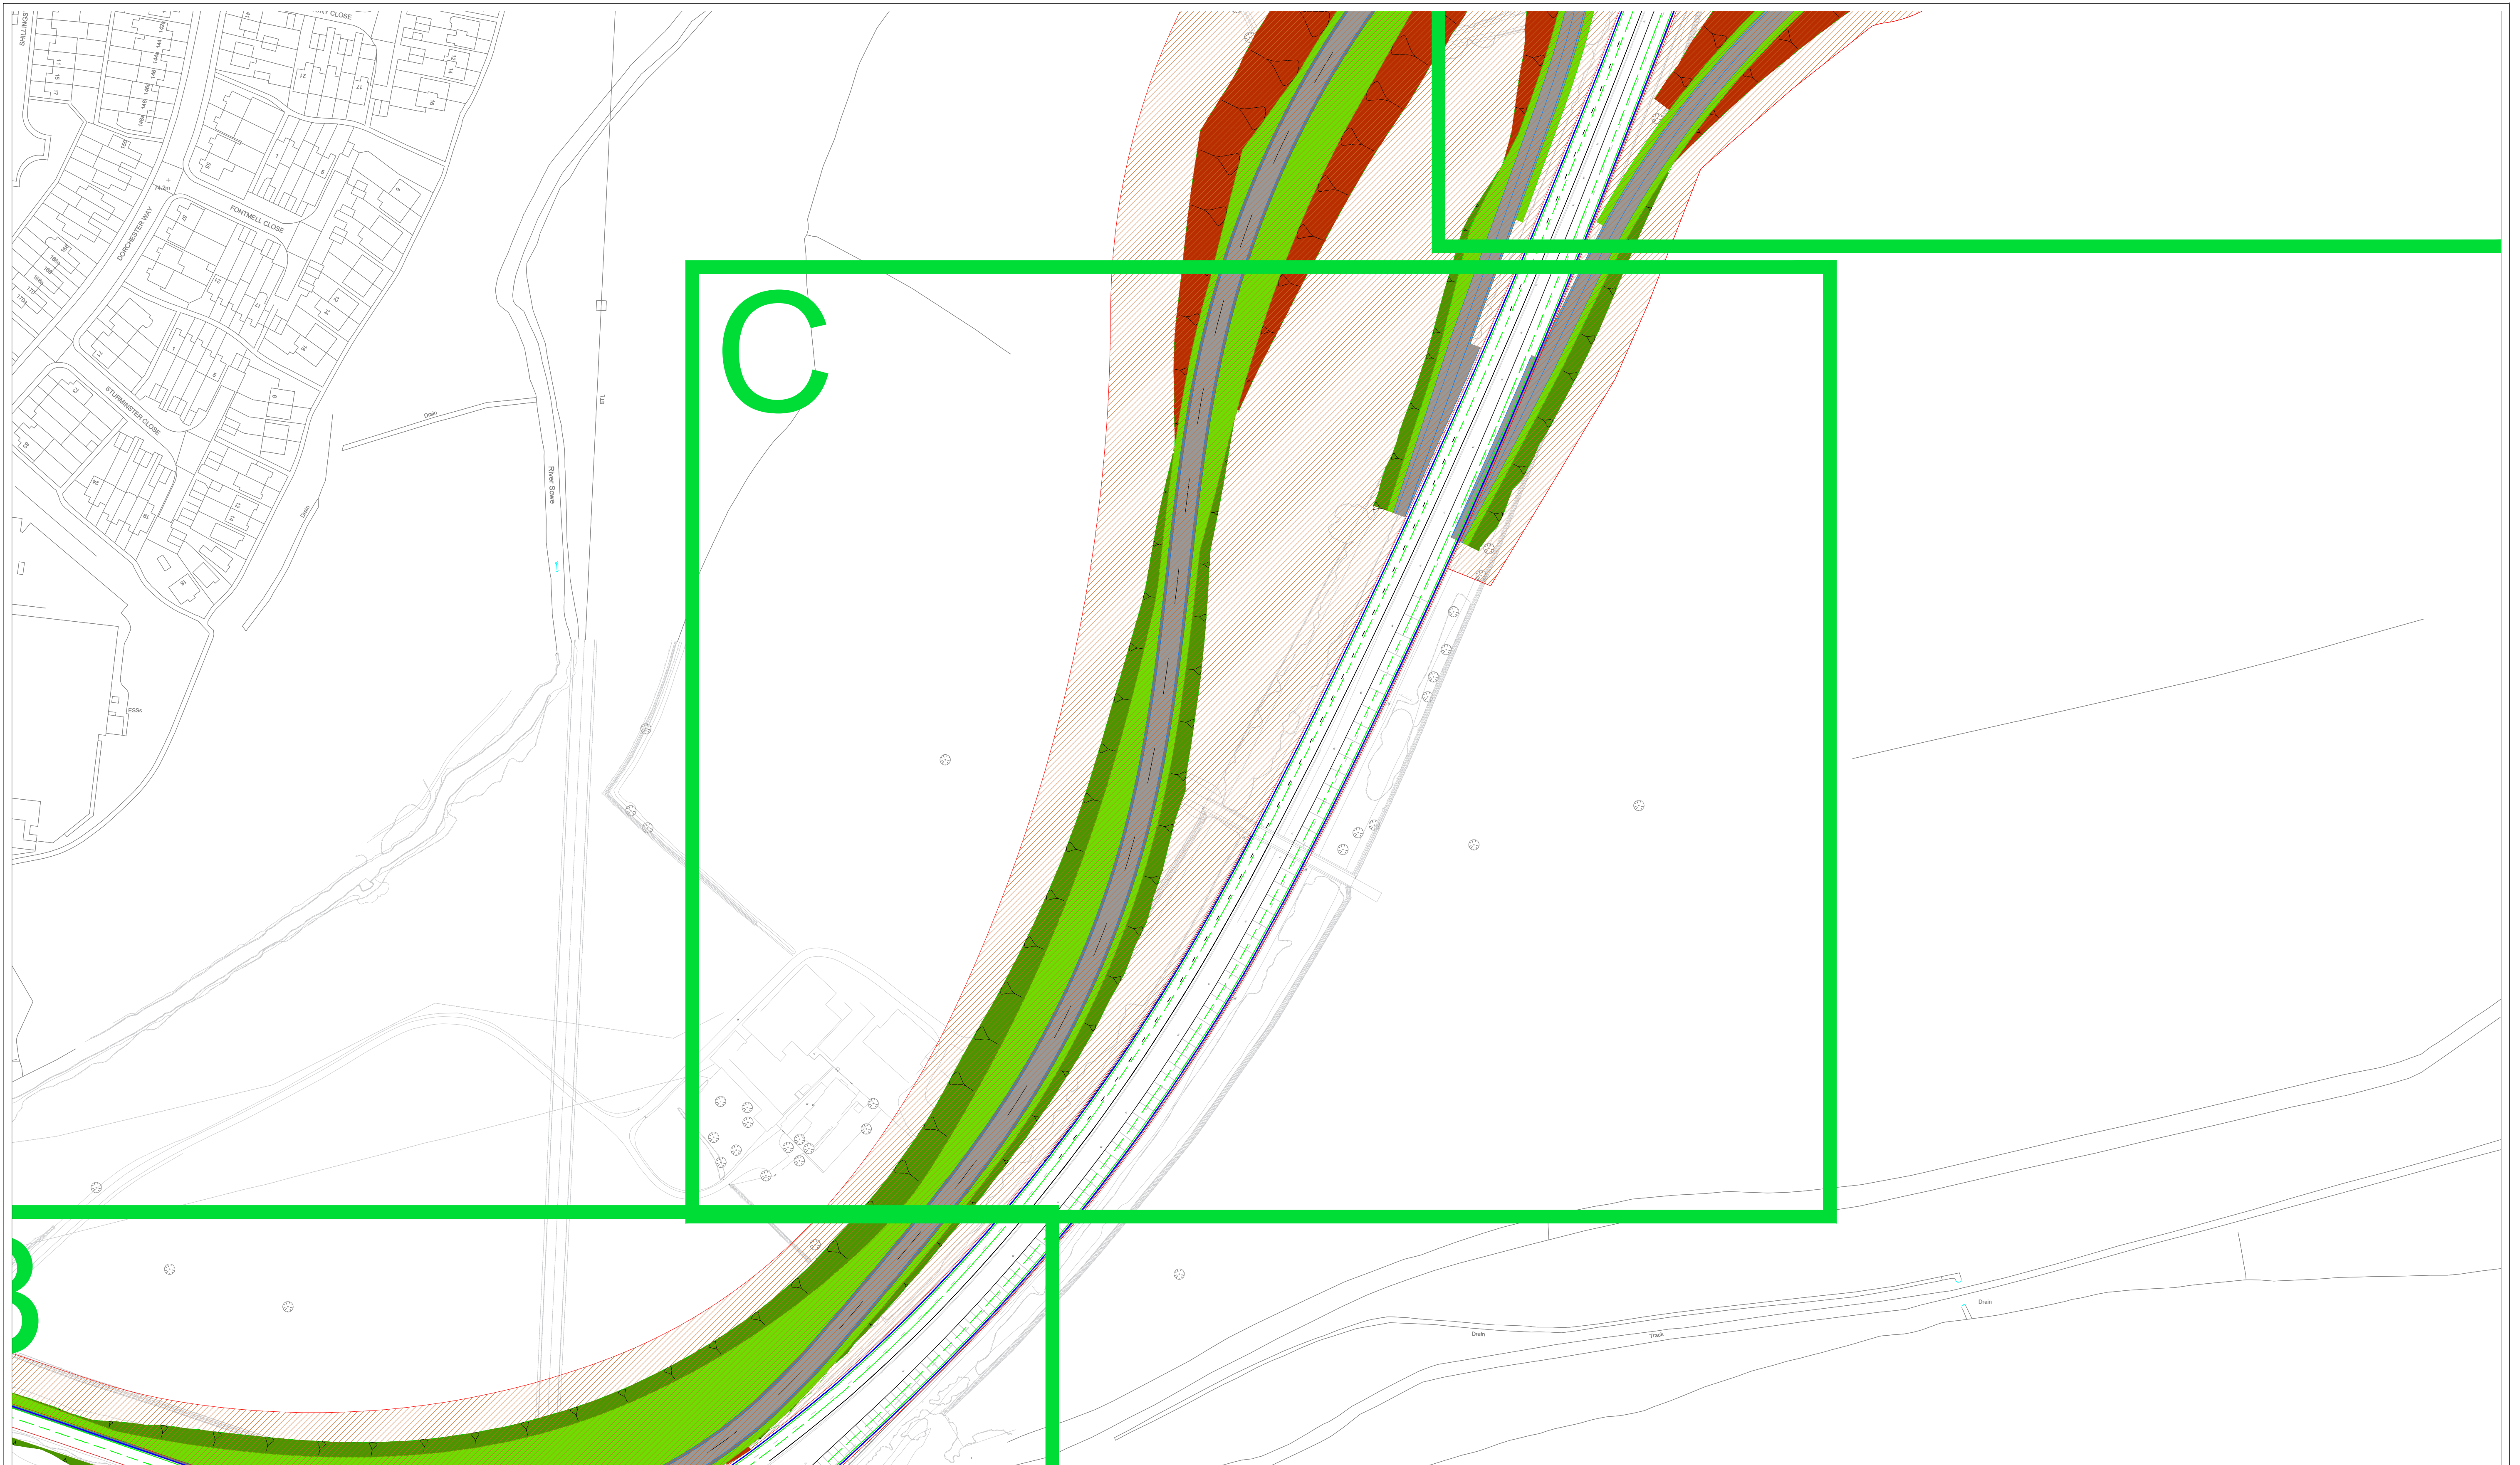

Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title:	Option 11 Phase 1 - C		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>		
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear		Date:	17/08/21	
	Revision details		Technical Support		Verified by:			Date:	
	Revision	-	Sheet No.	4 of 5	Validation by:			Date:	
	Revised by:	Rev:	Date:		Original size	A1	Scale	NTS	
					Designer Checklist No.:			HAZARD/RISK	HIGH/MED/LOW
					Technical Note & Design Commentary No.:				
					Associated Risk Assessment No.:				
					Layer Register No.:				
					DWG File Number No.:				



Client:	Project Title: A46 Walsgrave Junction Upgrade	Preliminary <input type="checkbox"/> For approval	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title: Option 11 Phase 1- D	For comment <input checked="" type="checkbox"/> Final Design		
	Drawing No. DRAFT OUTLINE 001	Drawn by: Ed Menear Date: 17/08/21	1	
	Revision details	Verified by: Date:		
	Sheet No. 5 of 5	Validation by: Date:		
		Original size A1 Scale NTS		
		Technical Support		
		Designer Checklist No: xxx		
		Technical Note & Design Commentary No: xxx		
		Associated Risk Assessment No: xxx		
		Layer Register No: xxx		
		DWG File Number No: xxx		

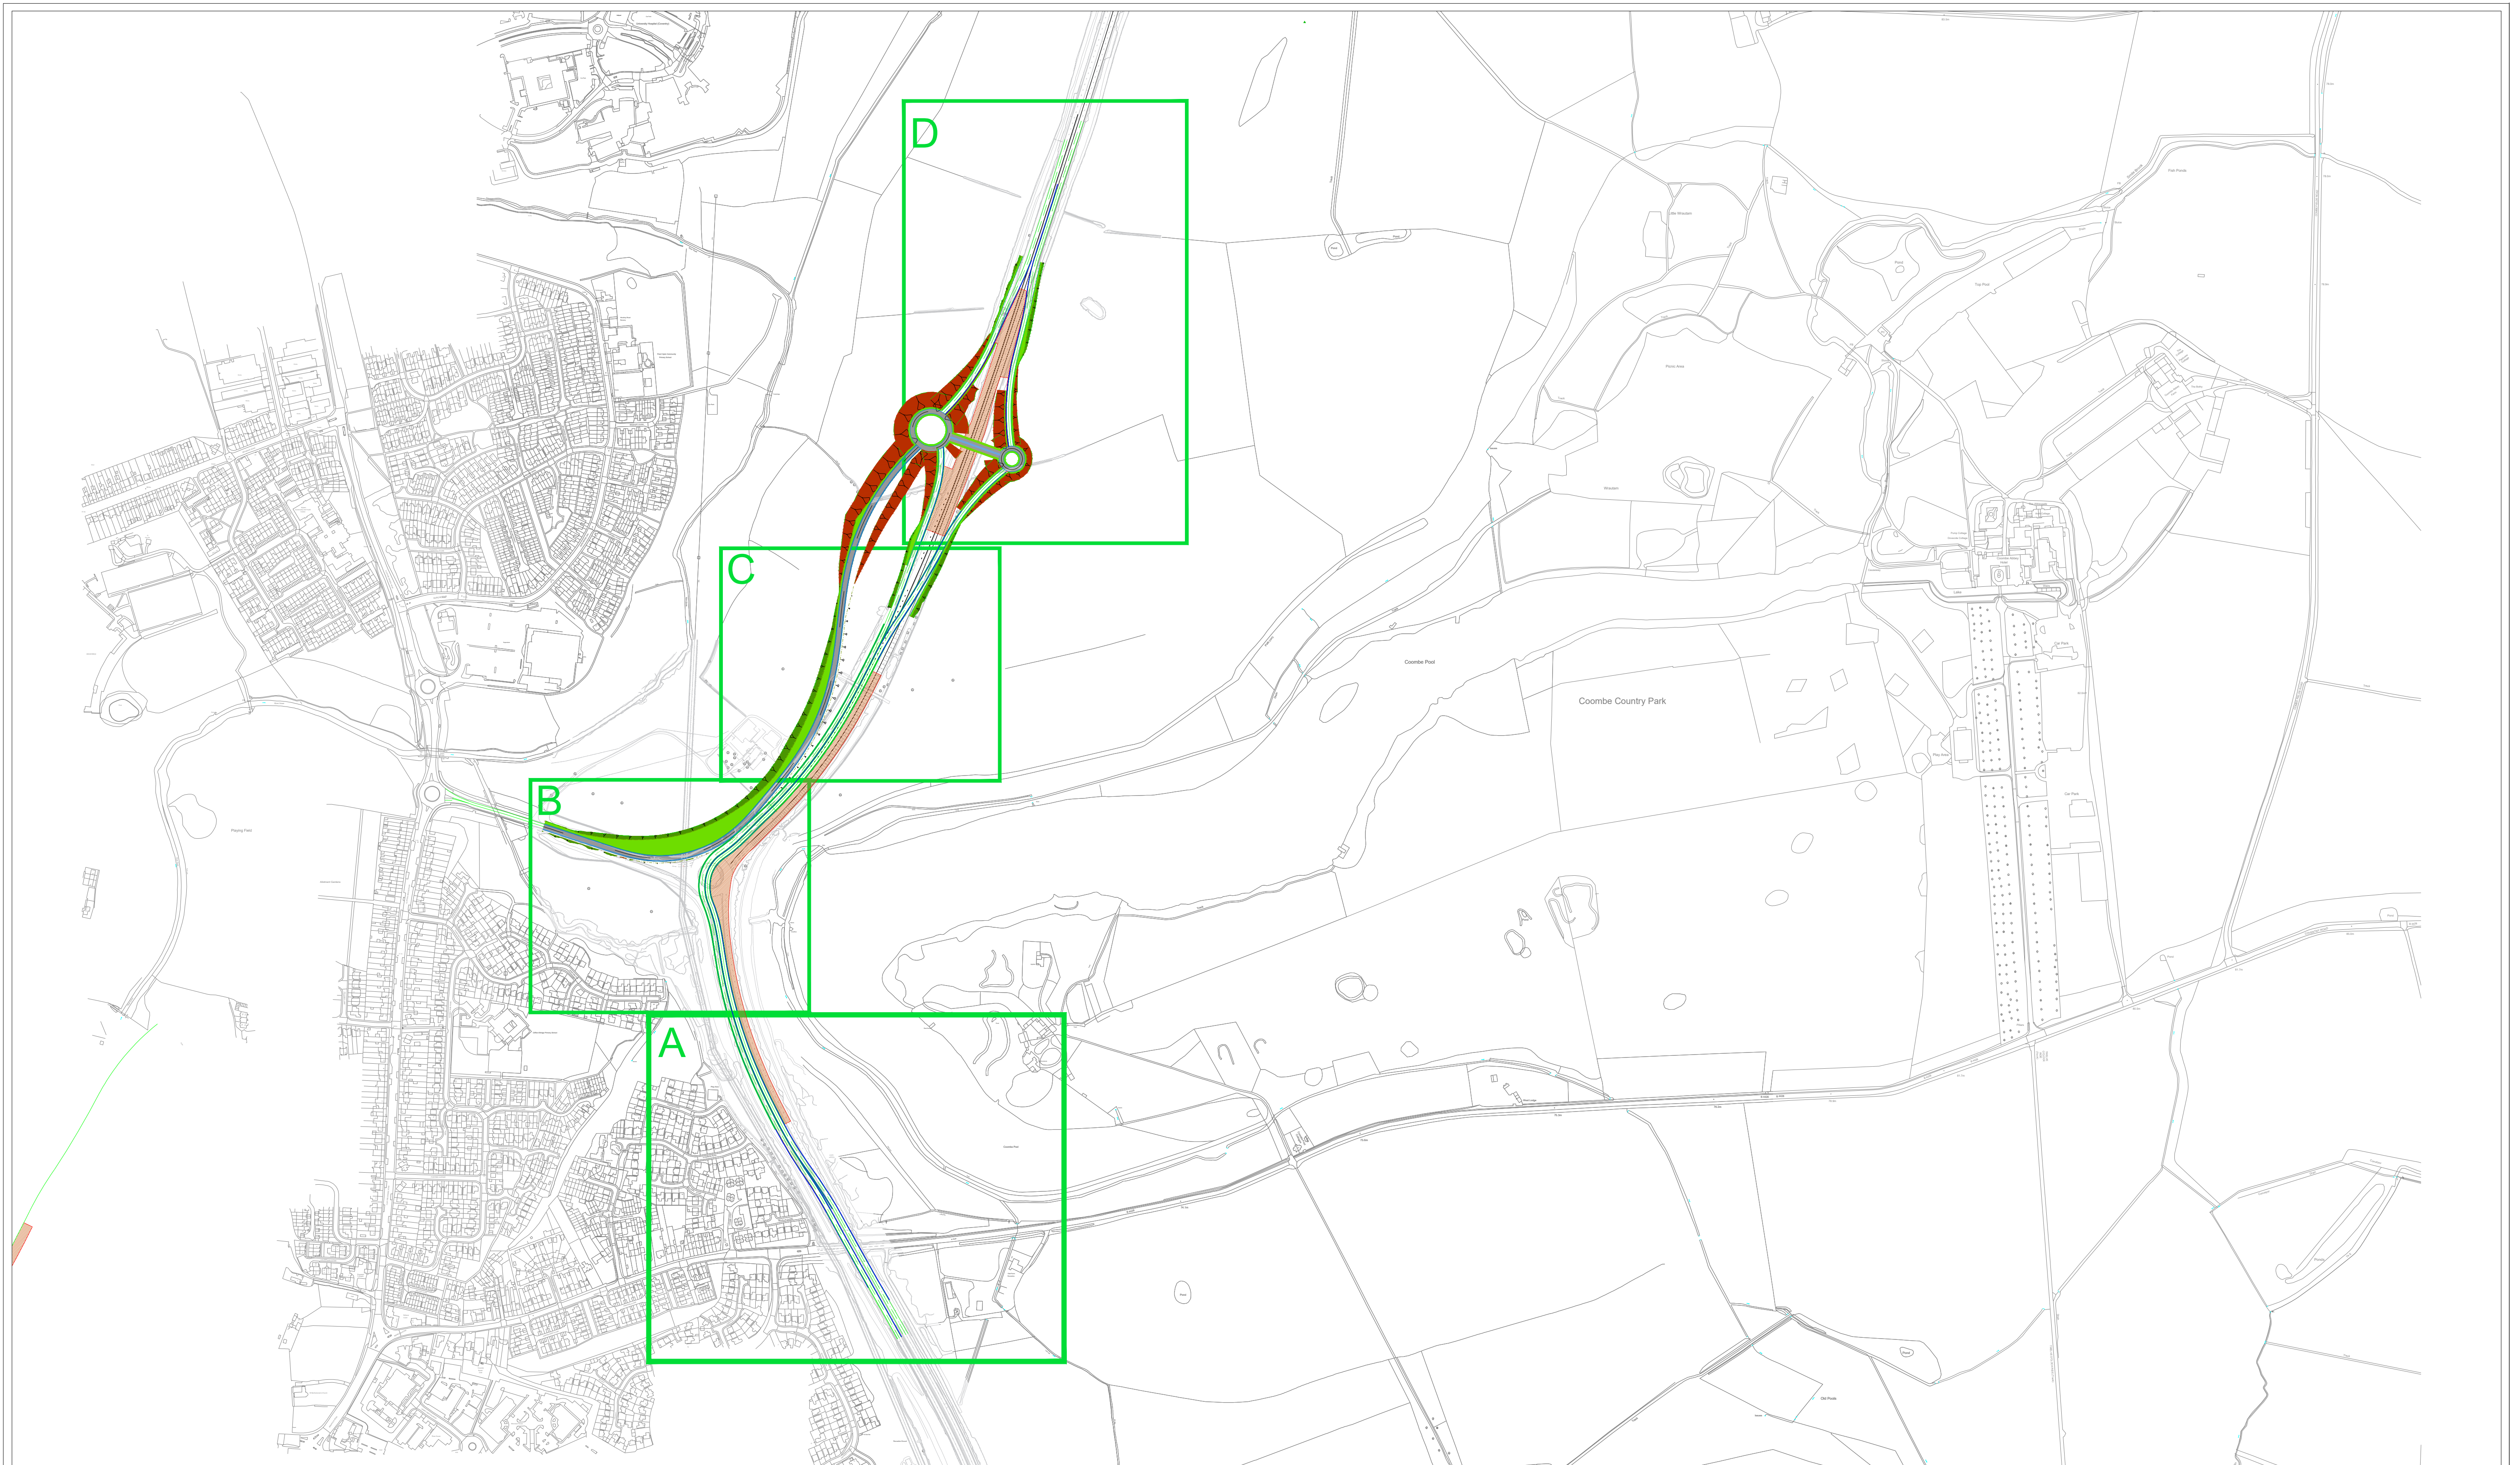

Client:

Project Title: **A46 Walsgrave Junction Upgrade**
 Drawing Title: **Option 11 Phase 2 Overview**
 Drawing No.: **DRAFT OUTLINE 001**
 Revision details
 Revision: - Sheet No. 1 of 5
 Revised by: Rev: Date:

Preliminary For approval
 For comment Final Design
 Drawn by: **Ed Menear** Date: **17/08/21**
 Verified by: Date:
 Validation by: Date:
 Original size **A1** Scale **NTS**
 Designer Checklist No: xxx
 Technical Note & Design Commentary No: xxx
 Associated Risk Assessment No: xxx
 Layer Register No: xxx
 DWG File Number No: xxx


IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX

HAZARD/RISK	HIGH/MED/LOW


KEY:




Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:	
	Drawing Title:	Option 11 Phase 2 - A		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>			
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear		Date:	17/08/21	HAZARD/RISK	
	Revision details			Verified by:			Date:			
	Revision	-	Sheet No. 2 of 5	Validation by:			Date:		HIGH/MED/LOW	
	Revised by:	Rev:	Date:	Original size	A1	Scale	NTS			
				Technical Support						
				Designer Checklist No:	xxx					
				Technical Note & Design Commentary No:	xxx					
				Associated Risk Assessment No:	xxx					
				Layer Register No:	xxx					
				DWG File Number No:	xxx					

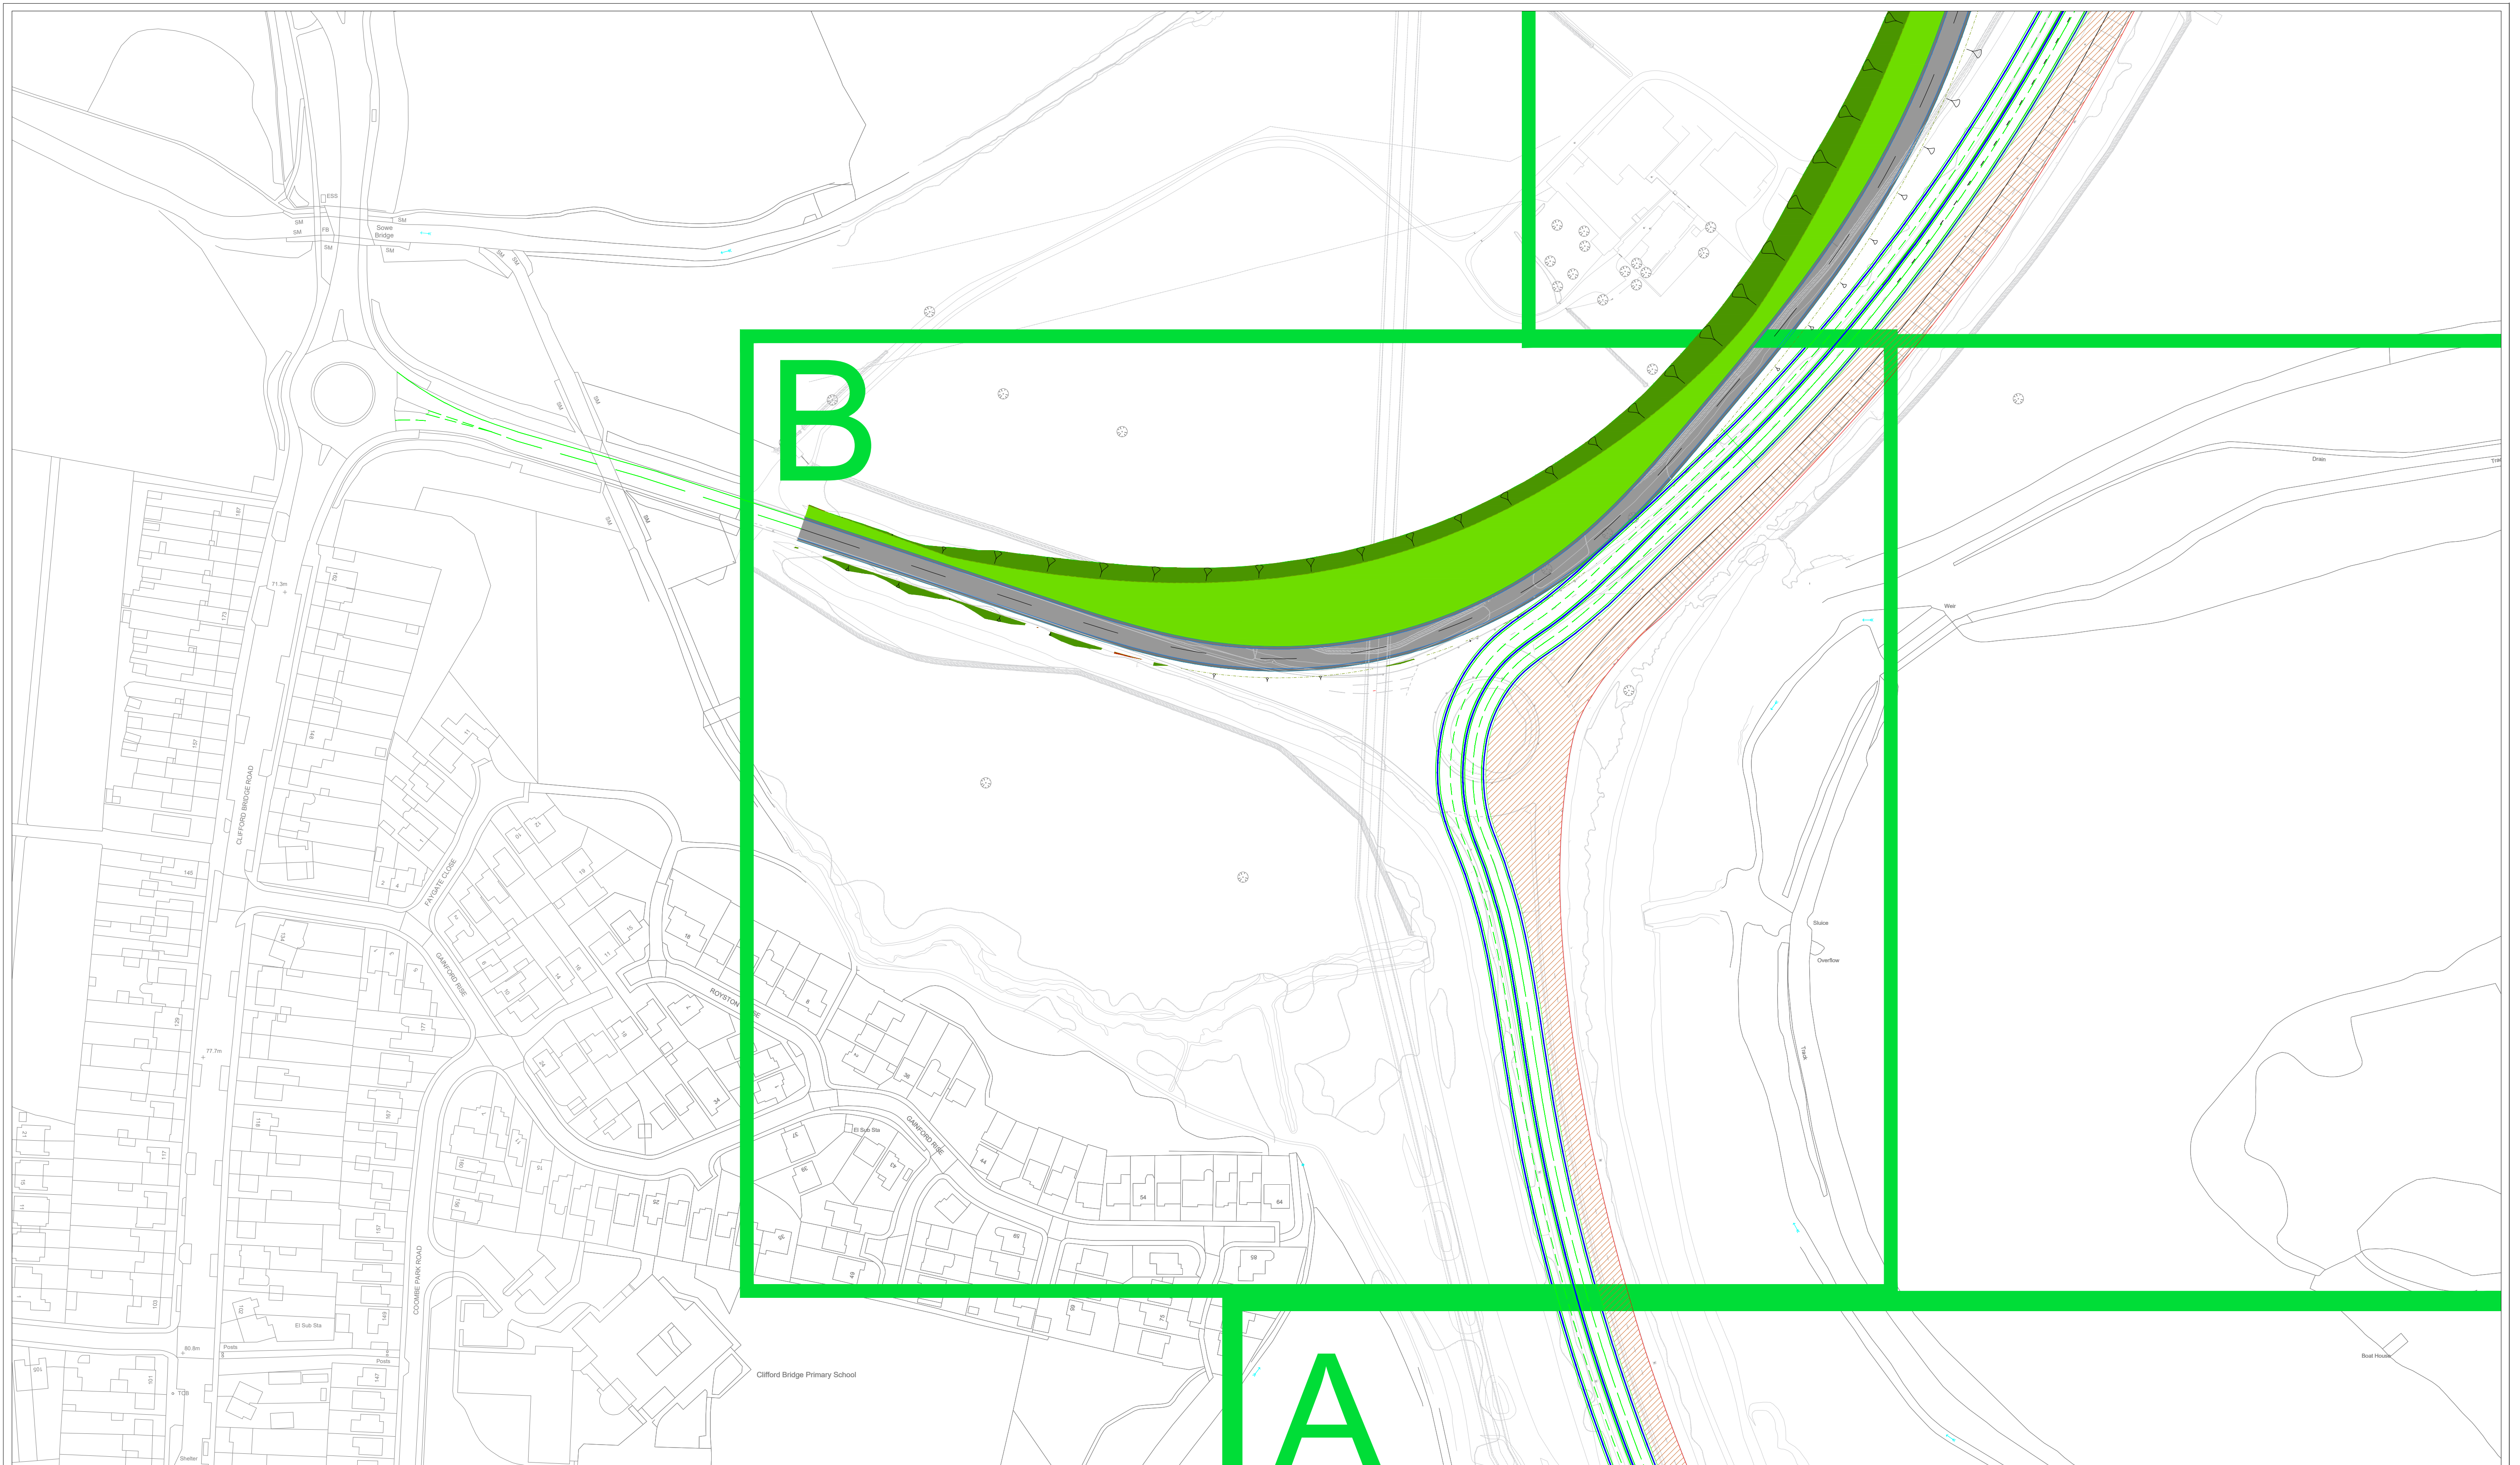


Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title:	Option 11 Phase 2 - B		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>		
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear	Date:	17/08/21	HAZARD/RISK	HIGH/MED/LOW
	Revision details	Revision - Sheet No. 3 of 5		Verified by:		Date:			
				Validation by:		Date:		1	
				Original size	A1	Scale	NTS		
				Technical Support					
				Designer Checklist No.:	xxx				
				Technical Note & Design Commentary No.:	xxx				
				Associated Risk Assessment No.:	xxx				
				Layer Register No.:	xxx				
				DWG File Number No.:	xxx				

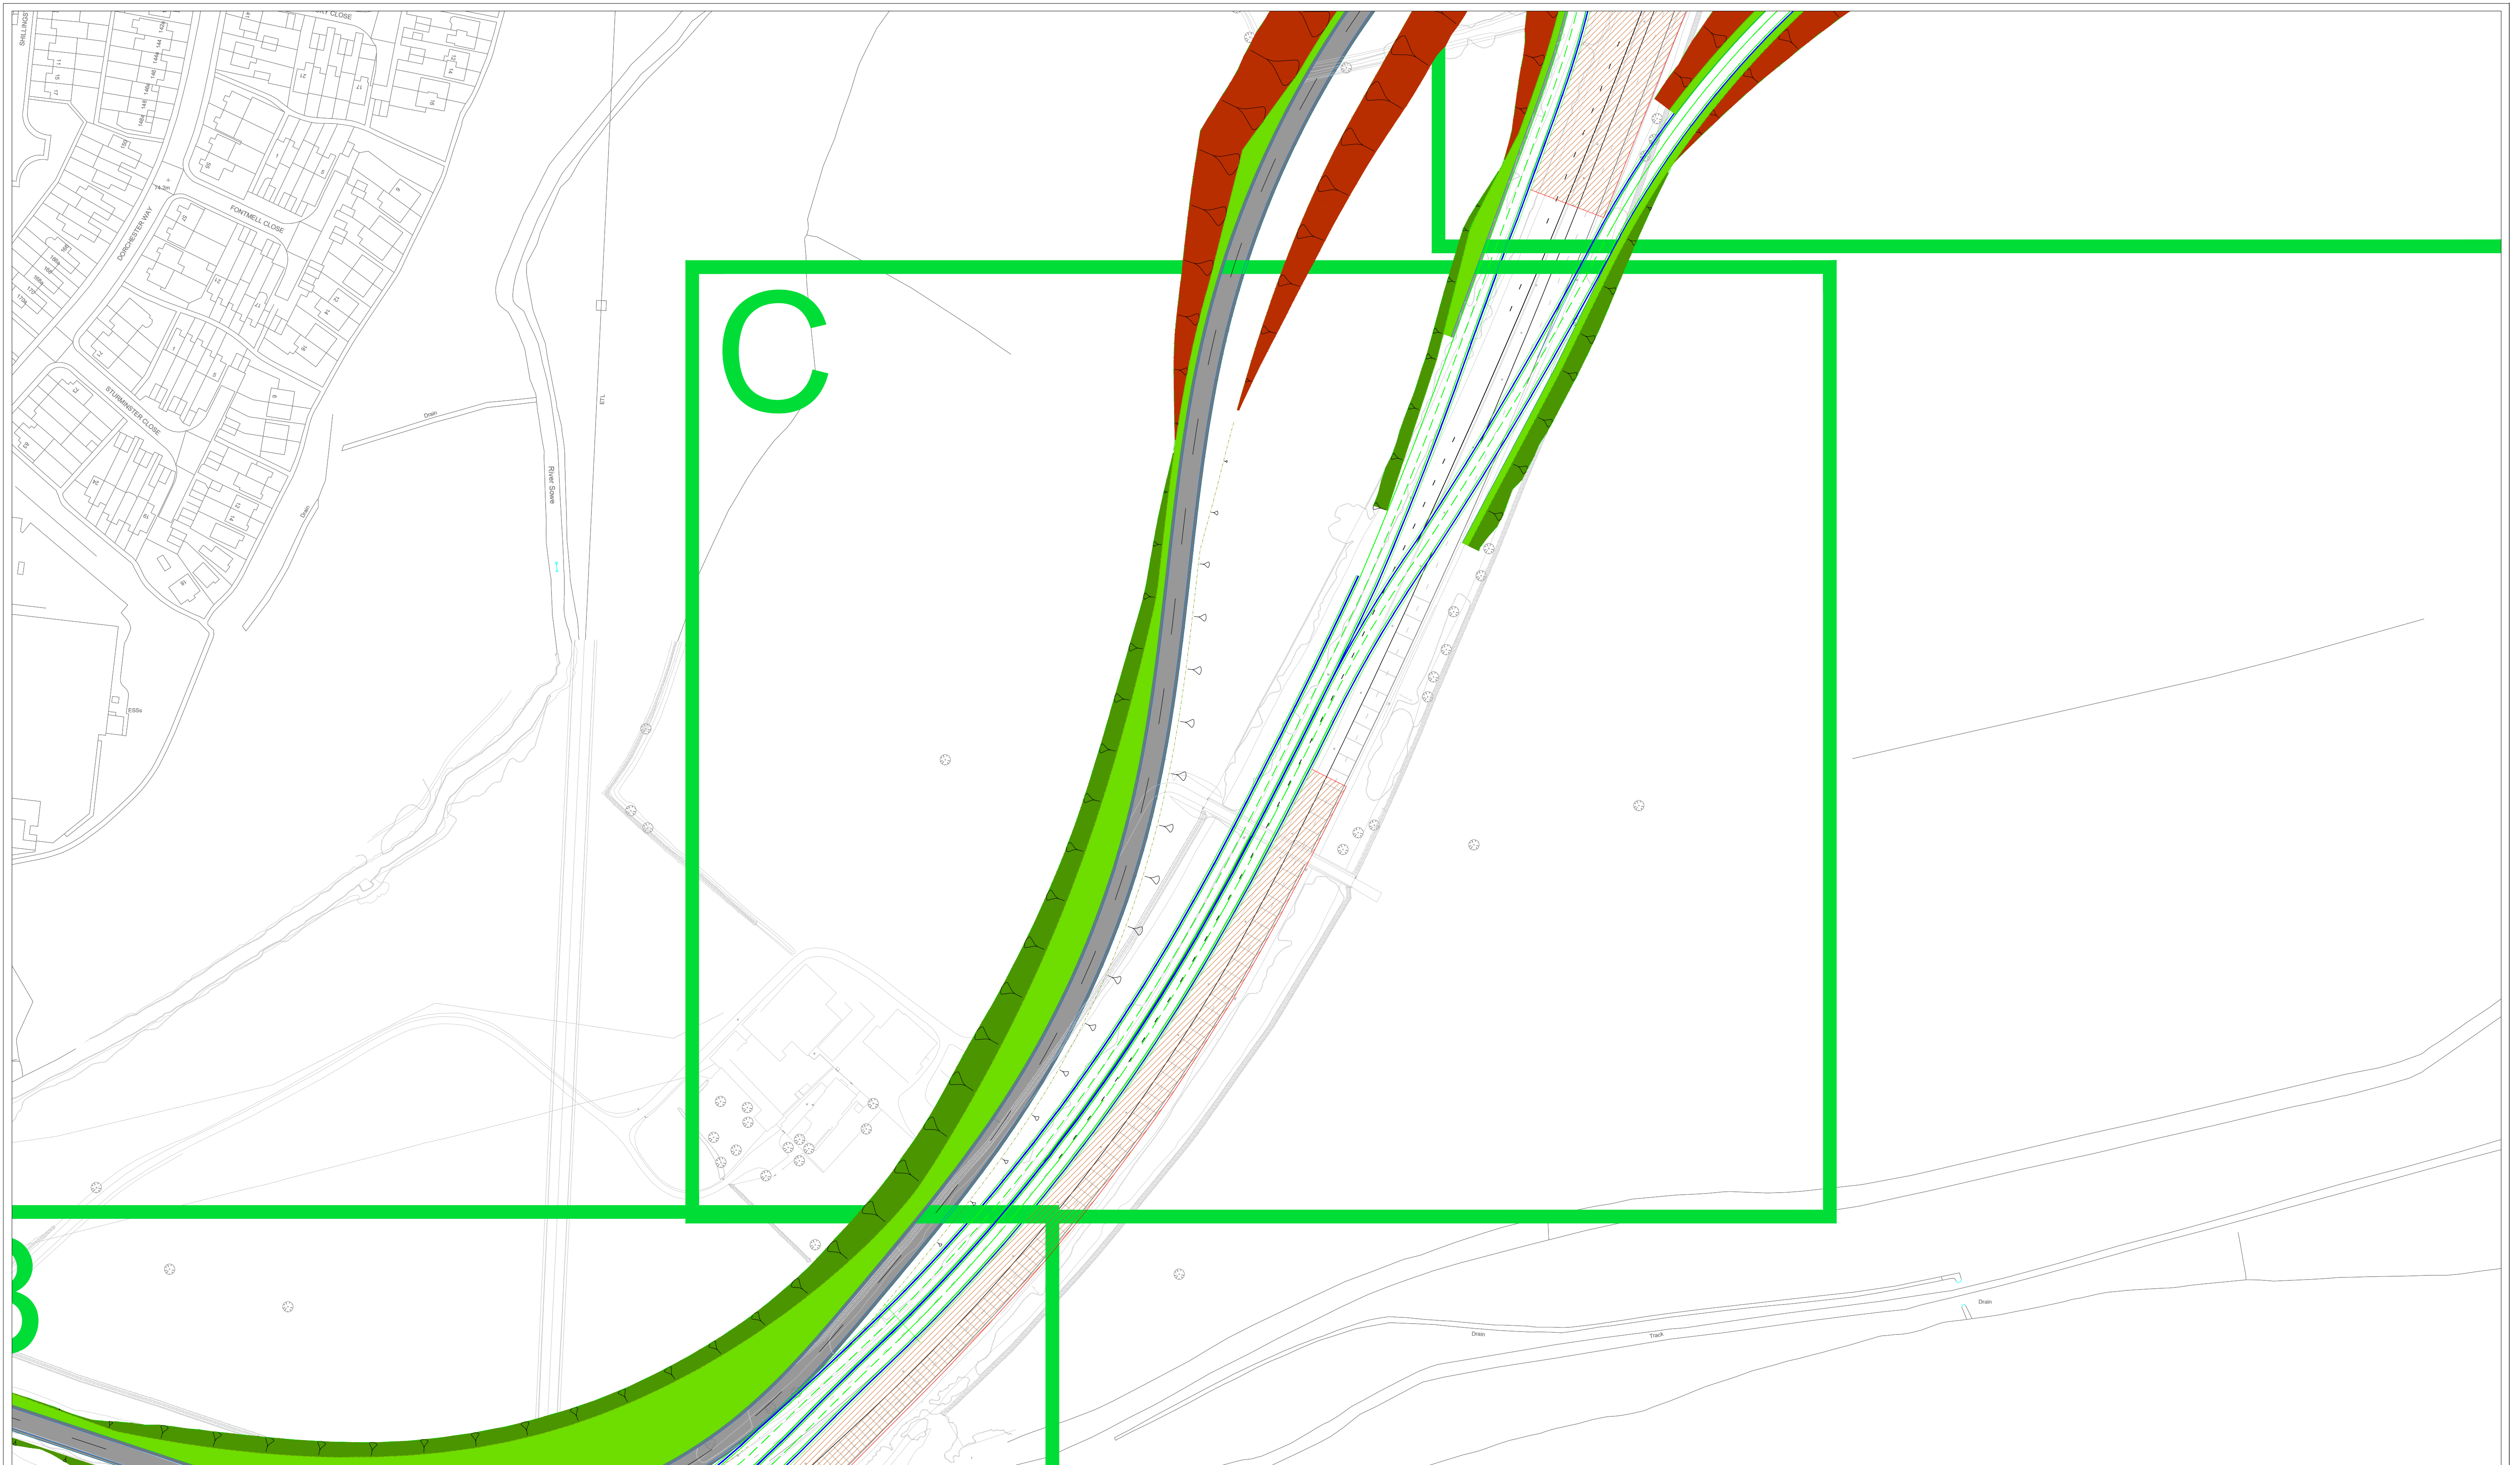


Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title:	Option 11 Phase 2- C		For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>		
	Drawing No.:	DRAFT OUTLINE 001		Drawn by:	Ed Menear		Date:	17/08/21	HAZARD/RISK
	Revision details	Revision		Verified by:			Date:		
		Sheet No. 4 of 5		Validation by:			Date:		HIGH/MED/LOW
				Original size	A1	Scale	NTS		
				Technical Support					
				Designer Checklist No.:	xxx				
				Technical Note & Design Commentary No.:	xxx				
				Associated Risk Assessment No.:	xxx				
				Layer Register No.:	xxx				
				DWG File Number No.:	xxx				

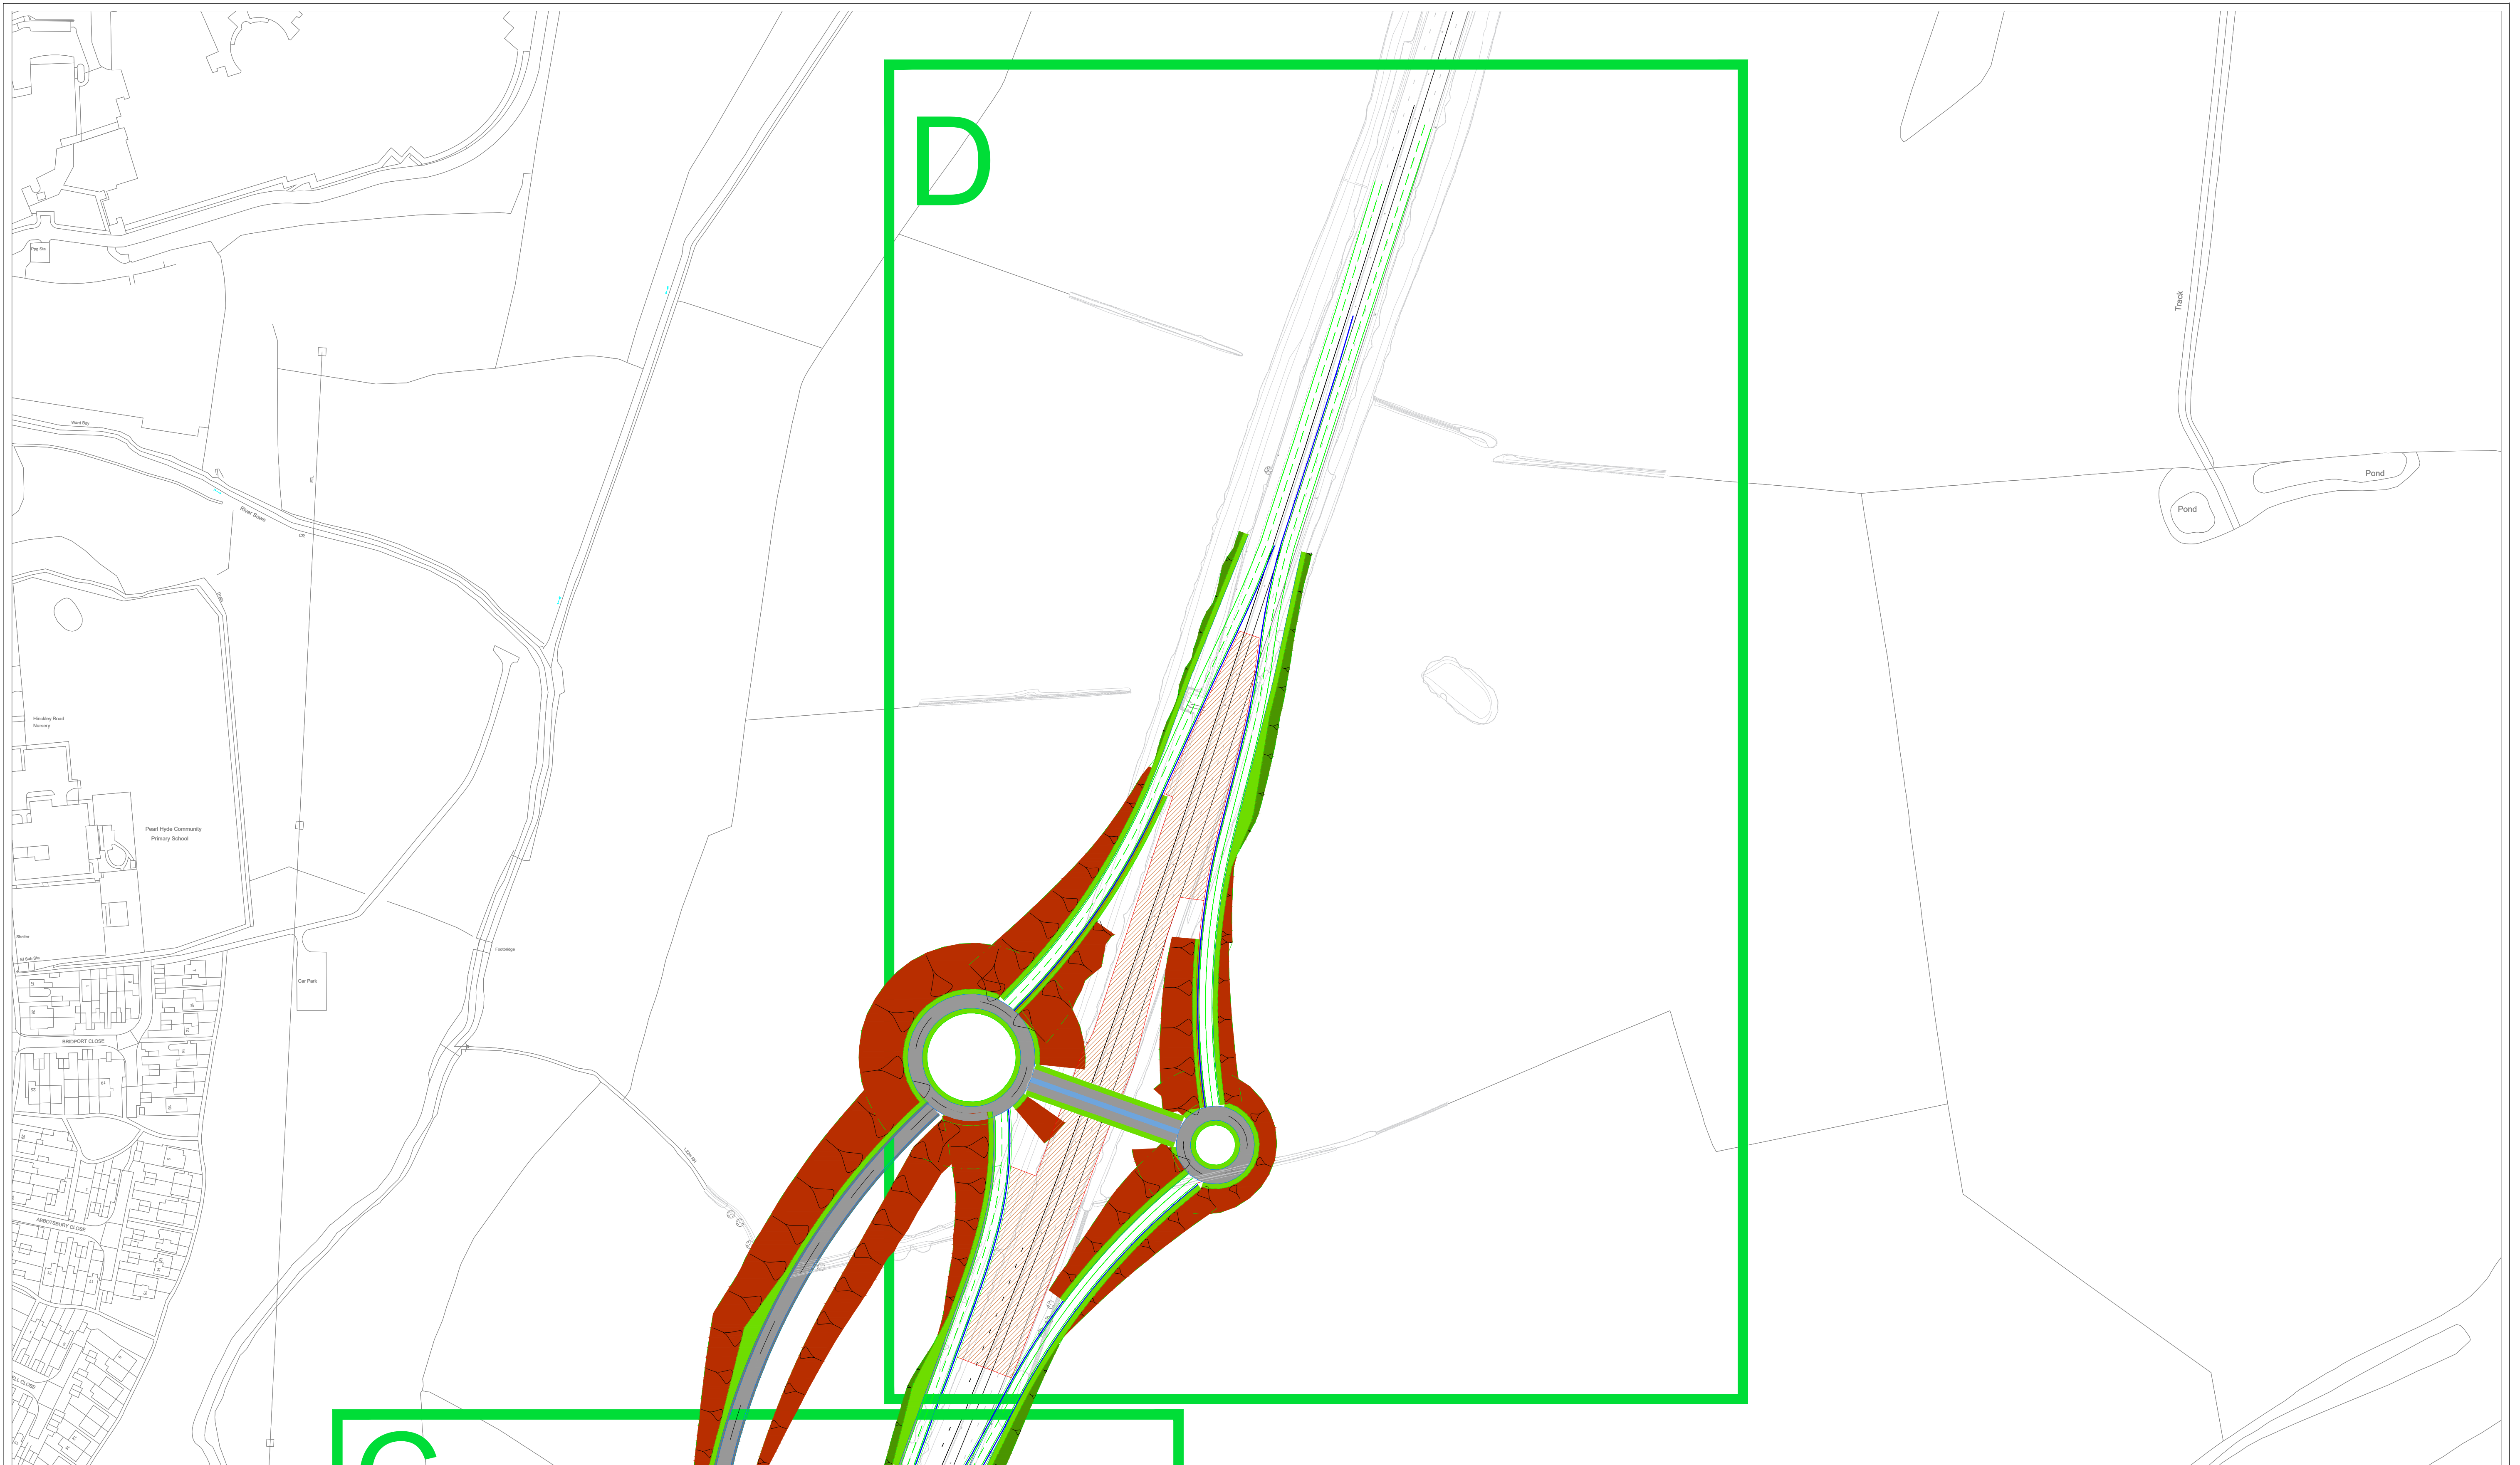

Client:	Project Title: A46 Walsgrave Junction Upgrade	Preliminary <input checked="" type="checkbox"/> For approval	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title: Option 11 Phase 2 - D	For comment <input checked="" type="checkbox"/> Final Design		
	Drawn by: Ed Menear	Date: 17/08/21	HAZARD/RISK	HIGH/MED/LOW
	Verified by:	Date:		
	Drawing No: DRAFT OUTLINE 001	Validation by:	Date:	
	Revision details	Original size A1	Scale NTS	
	Revision 1 Sheet No. 5 of 5	Technical Support		
	Revised by: Rev: Date:	Designer Checklist No: xxx		
		Technical Note & Design Commentary No: xxx		
		Associated Risk Assessment No: xxx		
		Layer Register No: xxx		
		DWG File Number No: xxx		

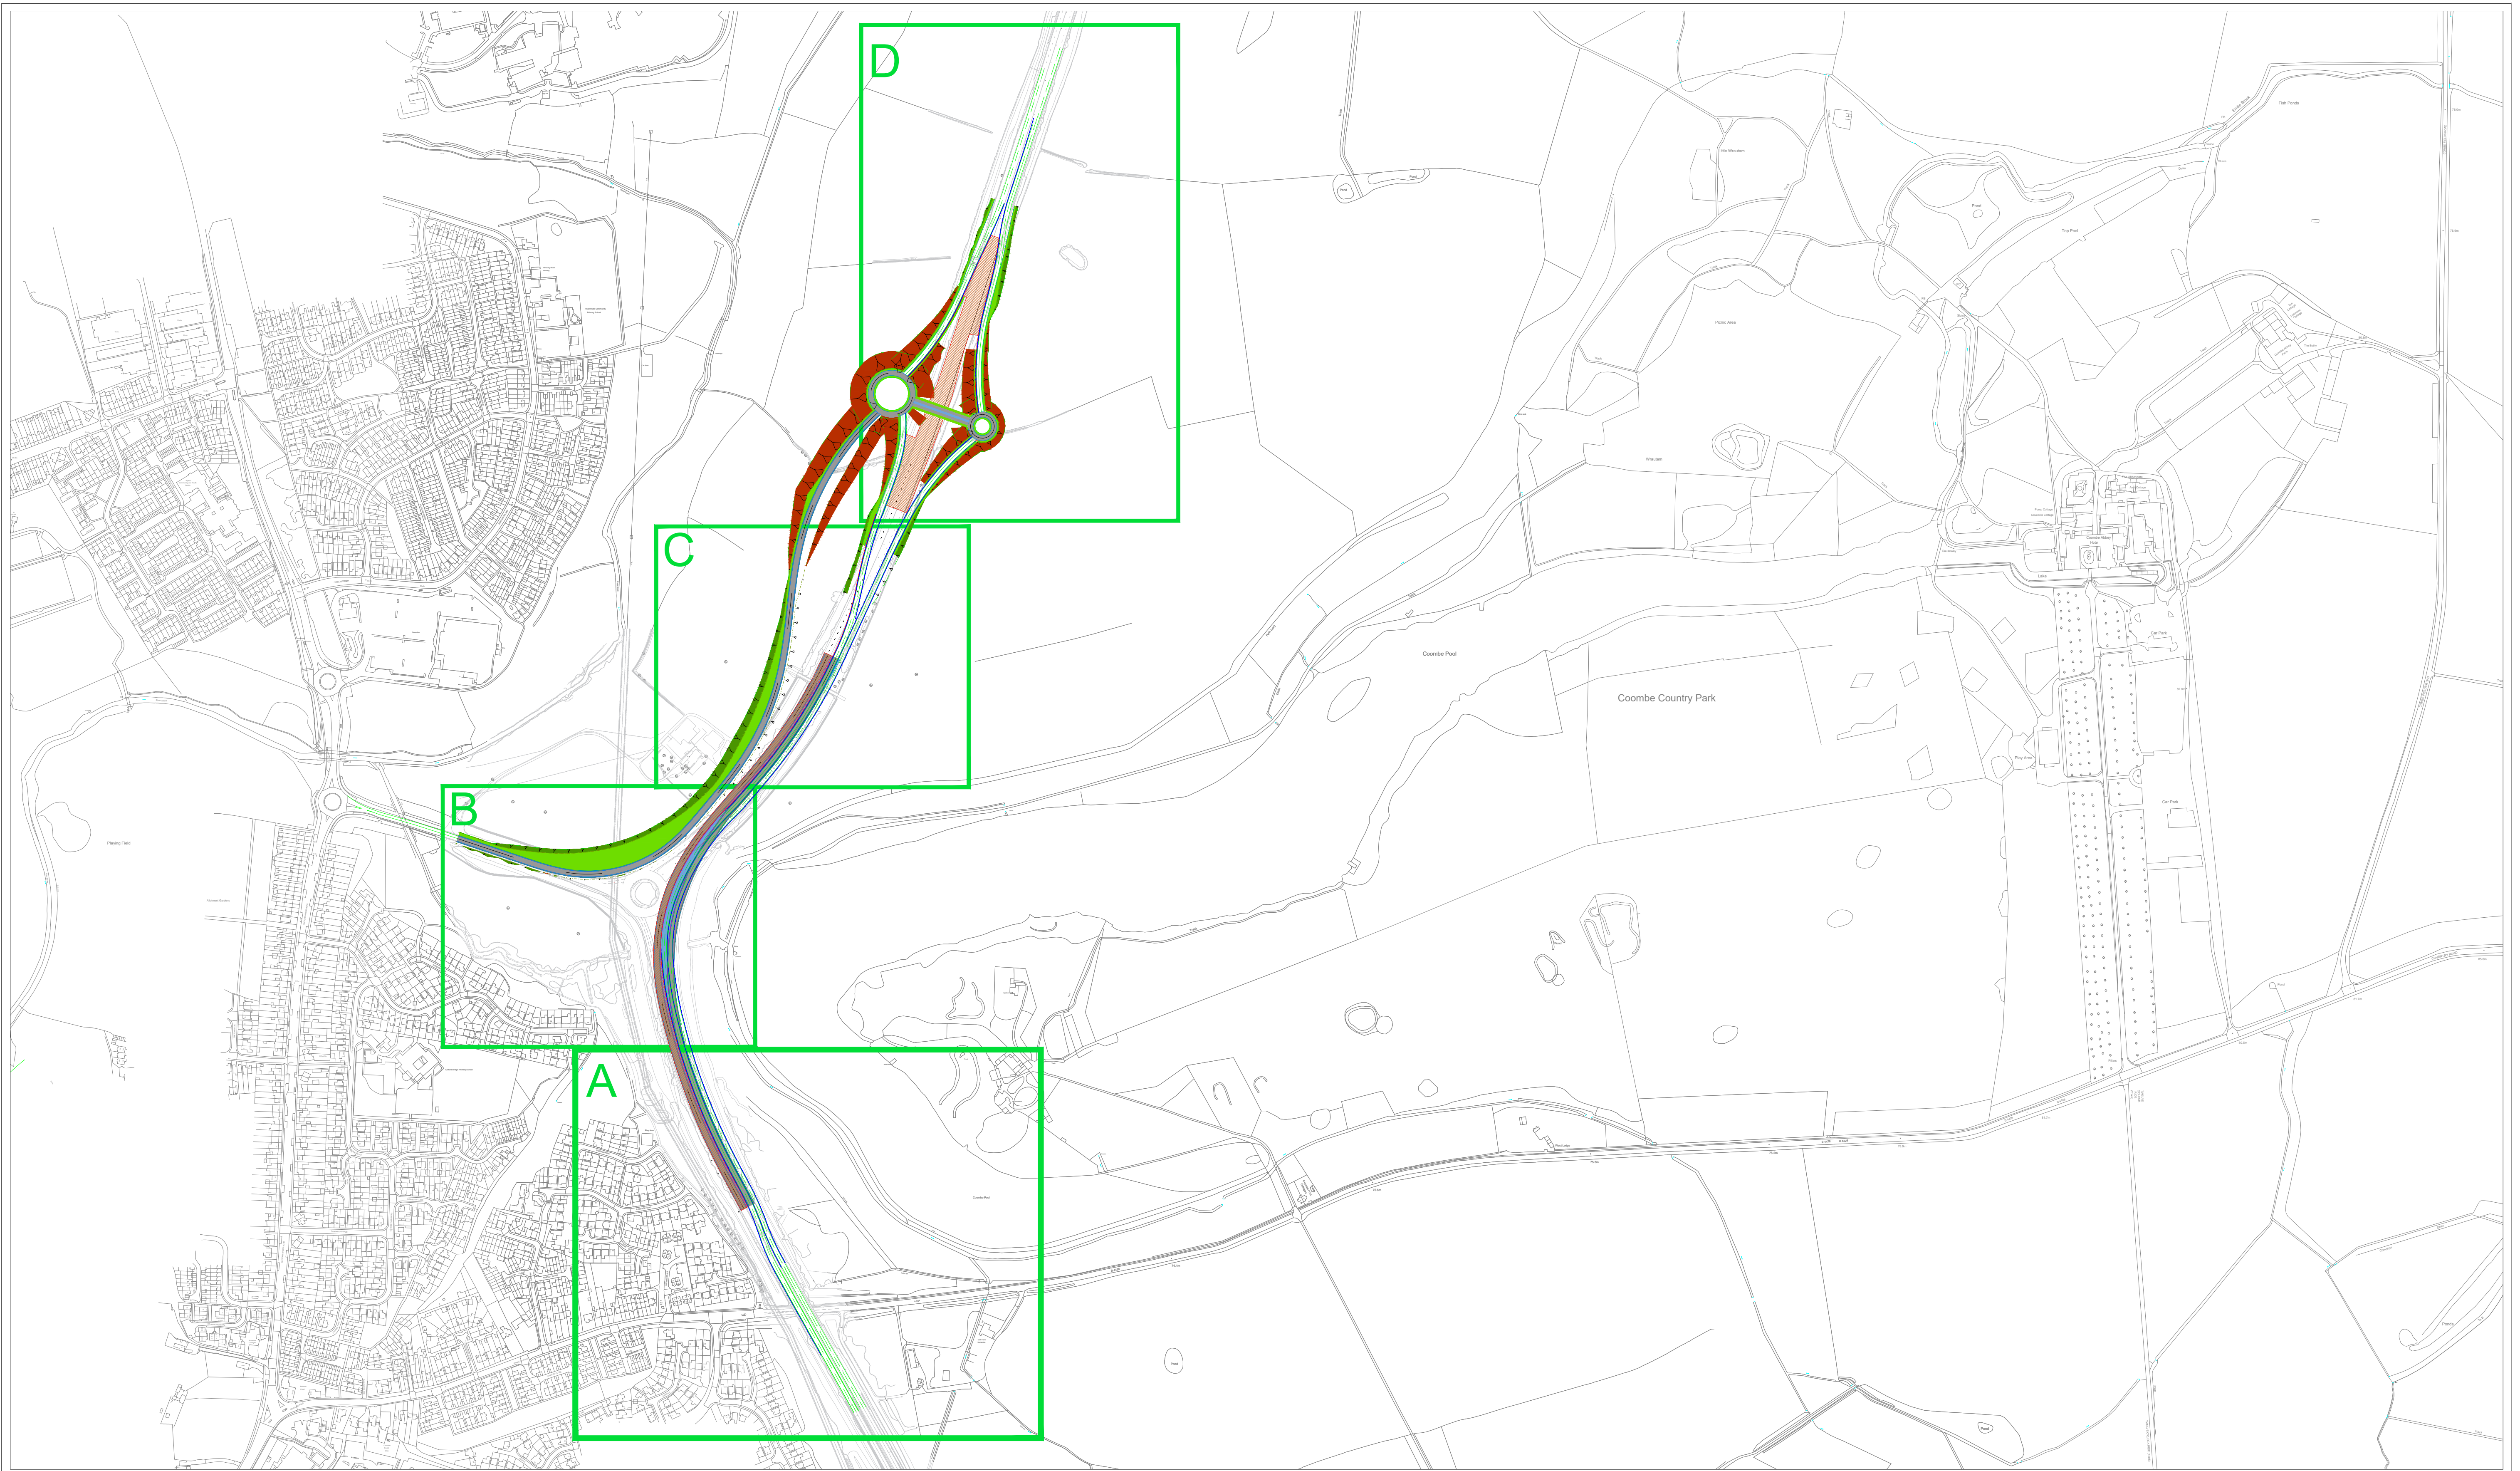


Client:	Project Title: A46 Walsgrave Junction Upgrade	Preliminary <input checked="" type="checkbox"/> For approval	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title: Option 11 Phase 3 Overview	For comment <input checked="" type="checkbox"/> Final Design		
	Drawing No. DRAFT OUTLINE 001	Drawn by: Ed Menear Date: 17/08/21	HIGH/MED/LOW	
	Revision details	Verified by: _____ Date: _____		
	Sheet No. 1 of 5	Validation by: _____ Date: _____		
		Original size A1 Scale NTS		
		Designer Checklist No: xxx		
		Technical Note & Design Commentary No: xxx		
		Associated Risk Assessment No: xxx		
		Layer Register No: xxx		
		DWG File Number No: xxx		

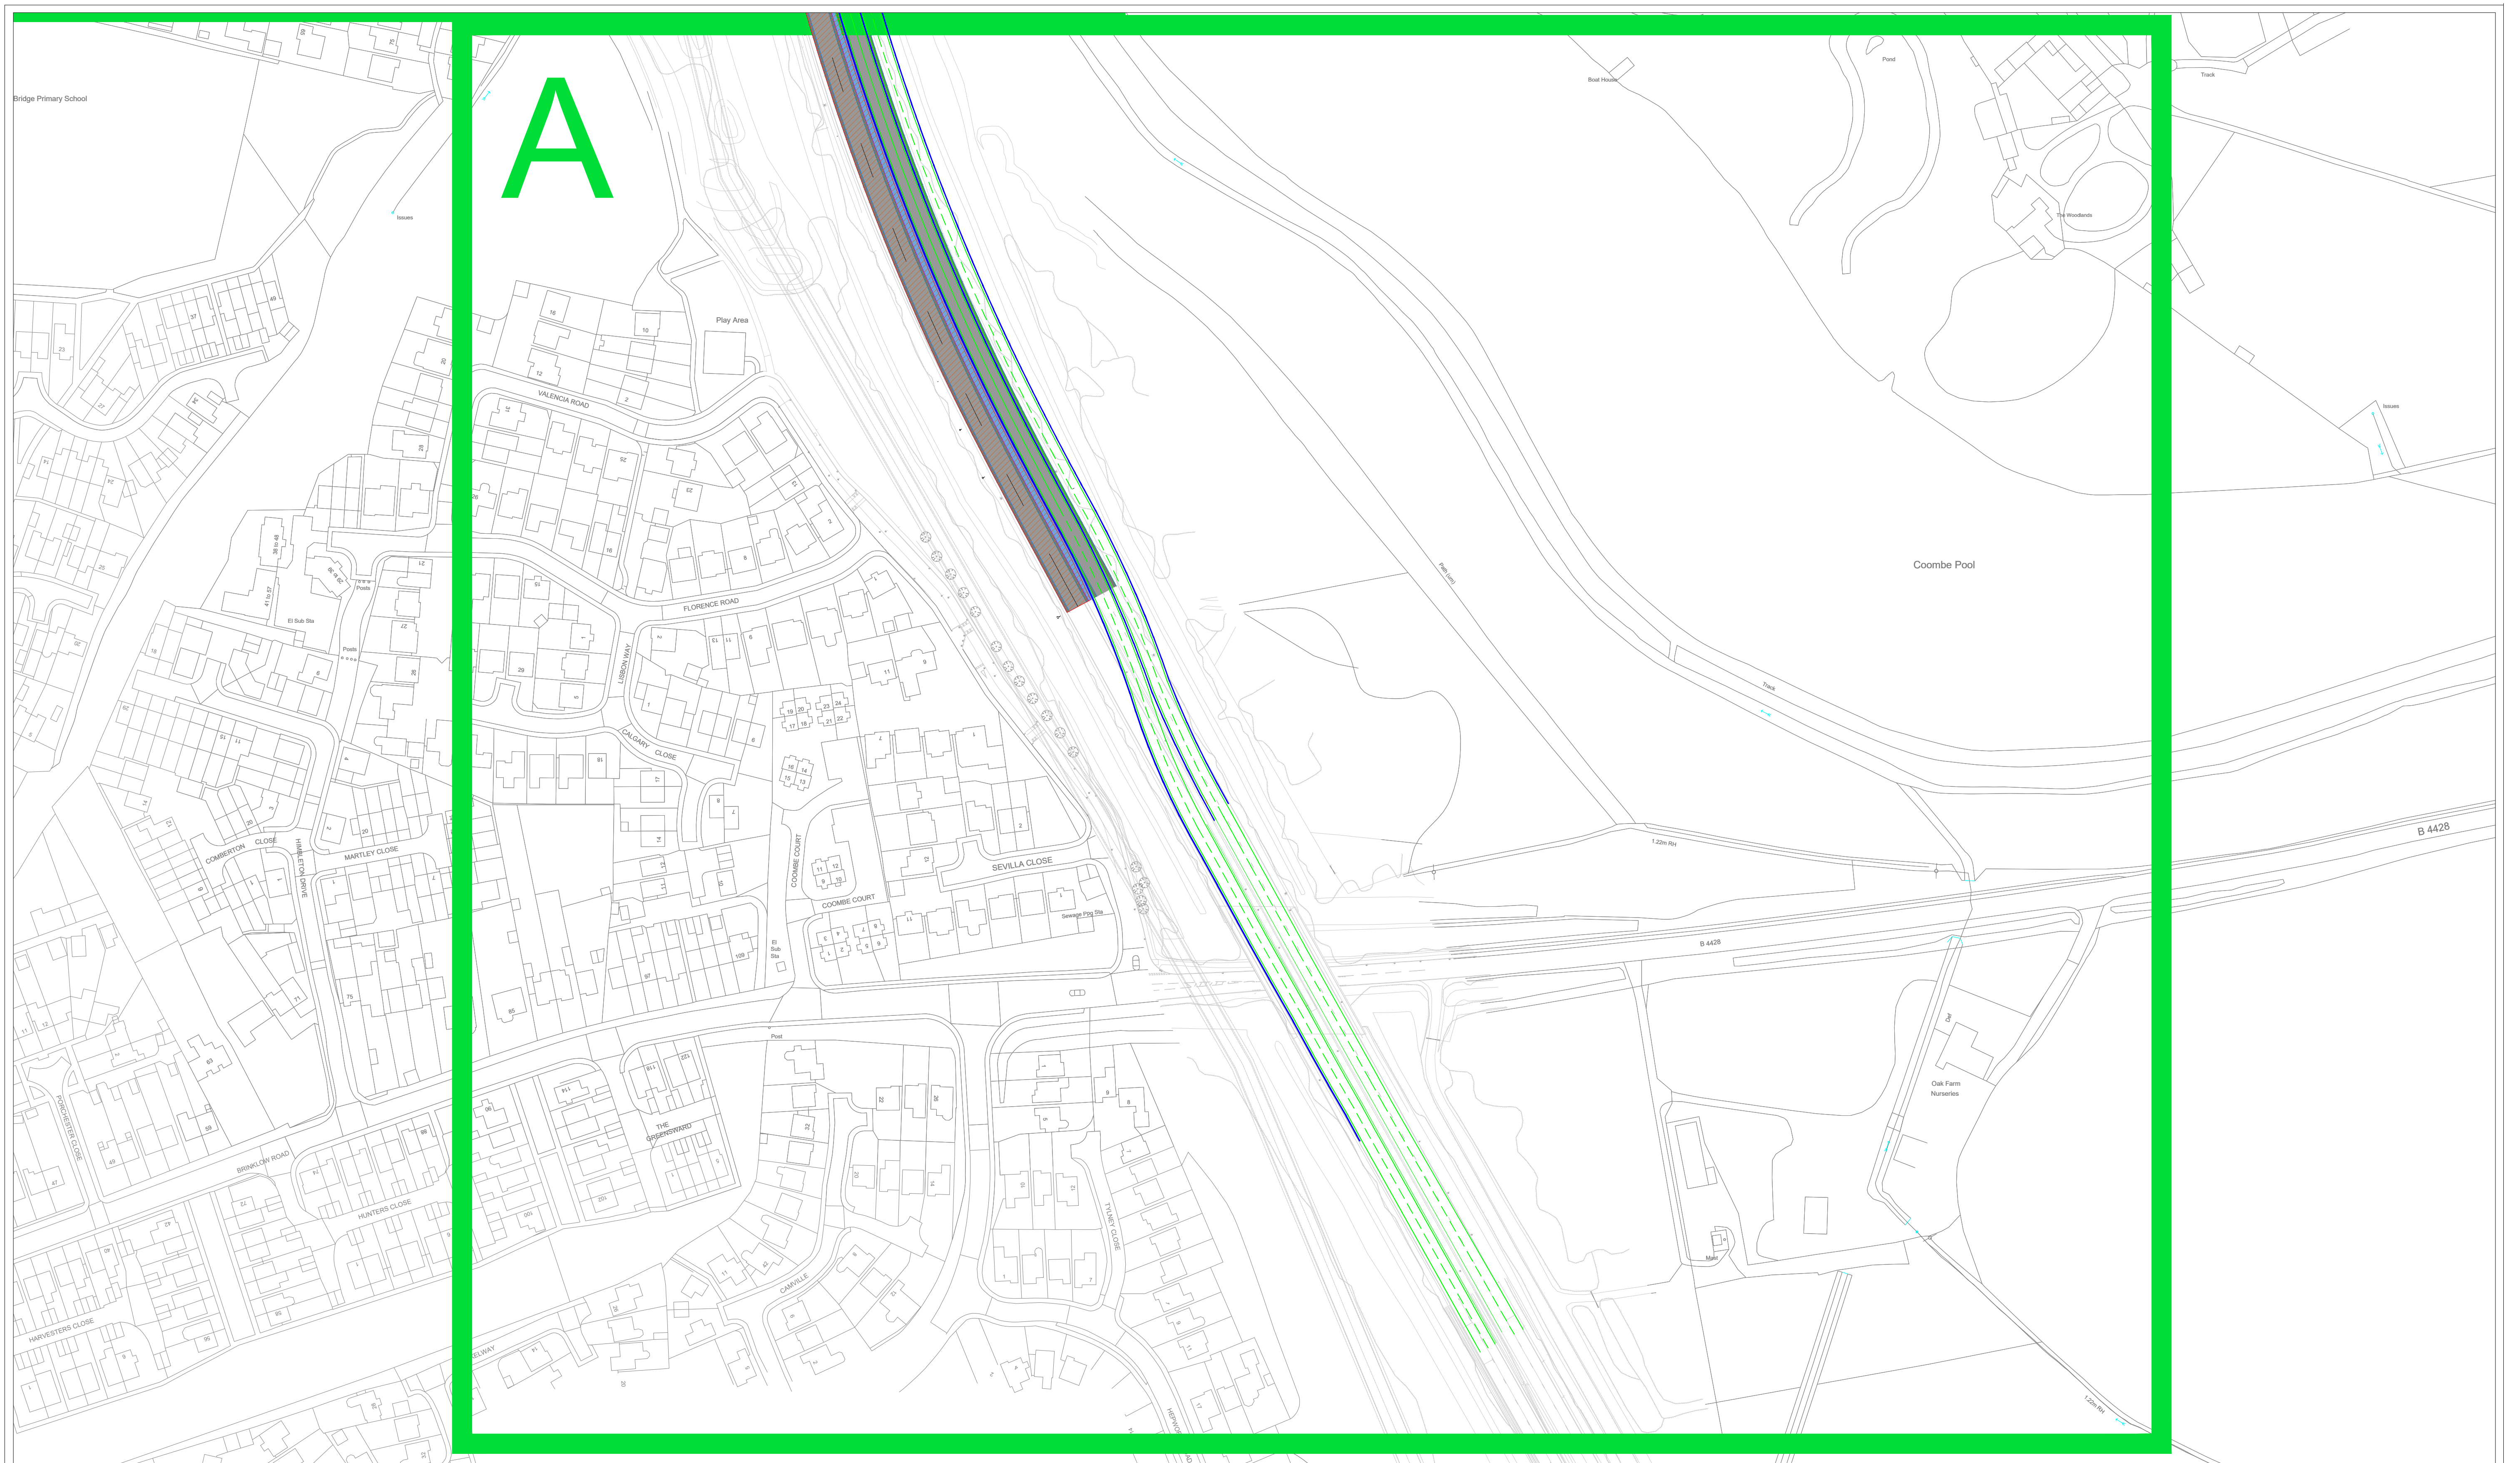

A

Client:	Project Title:	A46 Walsgrave Junction Upgrade		Preliminary For comment	<input type="checkbox"/>	For approval Final Design	<input checked="" type="checkbox"/>	IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	KEY:
	Drawing Title:	Option 11 Phase 3 - A		Drawn by:	Ed Menear	Date:	17/08/21		
	Drawing No.:	DRAFT OUTLINE 001		Verified by:		Date:			
	Revision details		Technical Support		Validation by:				
	Revision	Sheet No.	2 of 5	Original size	A1	Scale	NTS		
	Revised by:	Rev:	Date:	Designer Checklist No.:	xxx	Technical Note & Design Commentary No.:	xxx		
				Associated Risk Assessment No.:	xxx	Layer Register No.:	xxx		
				DWG File Number No.:	xxx				

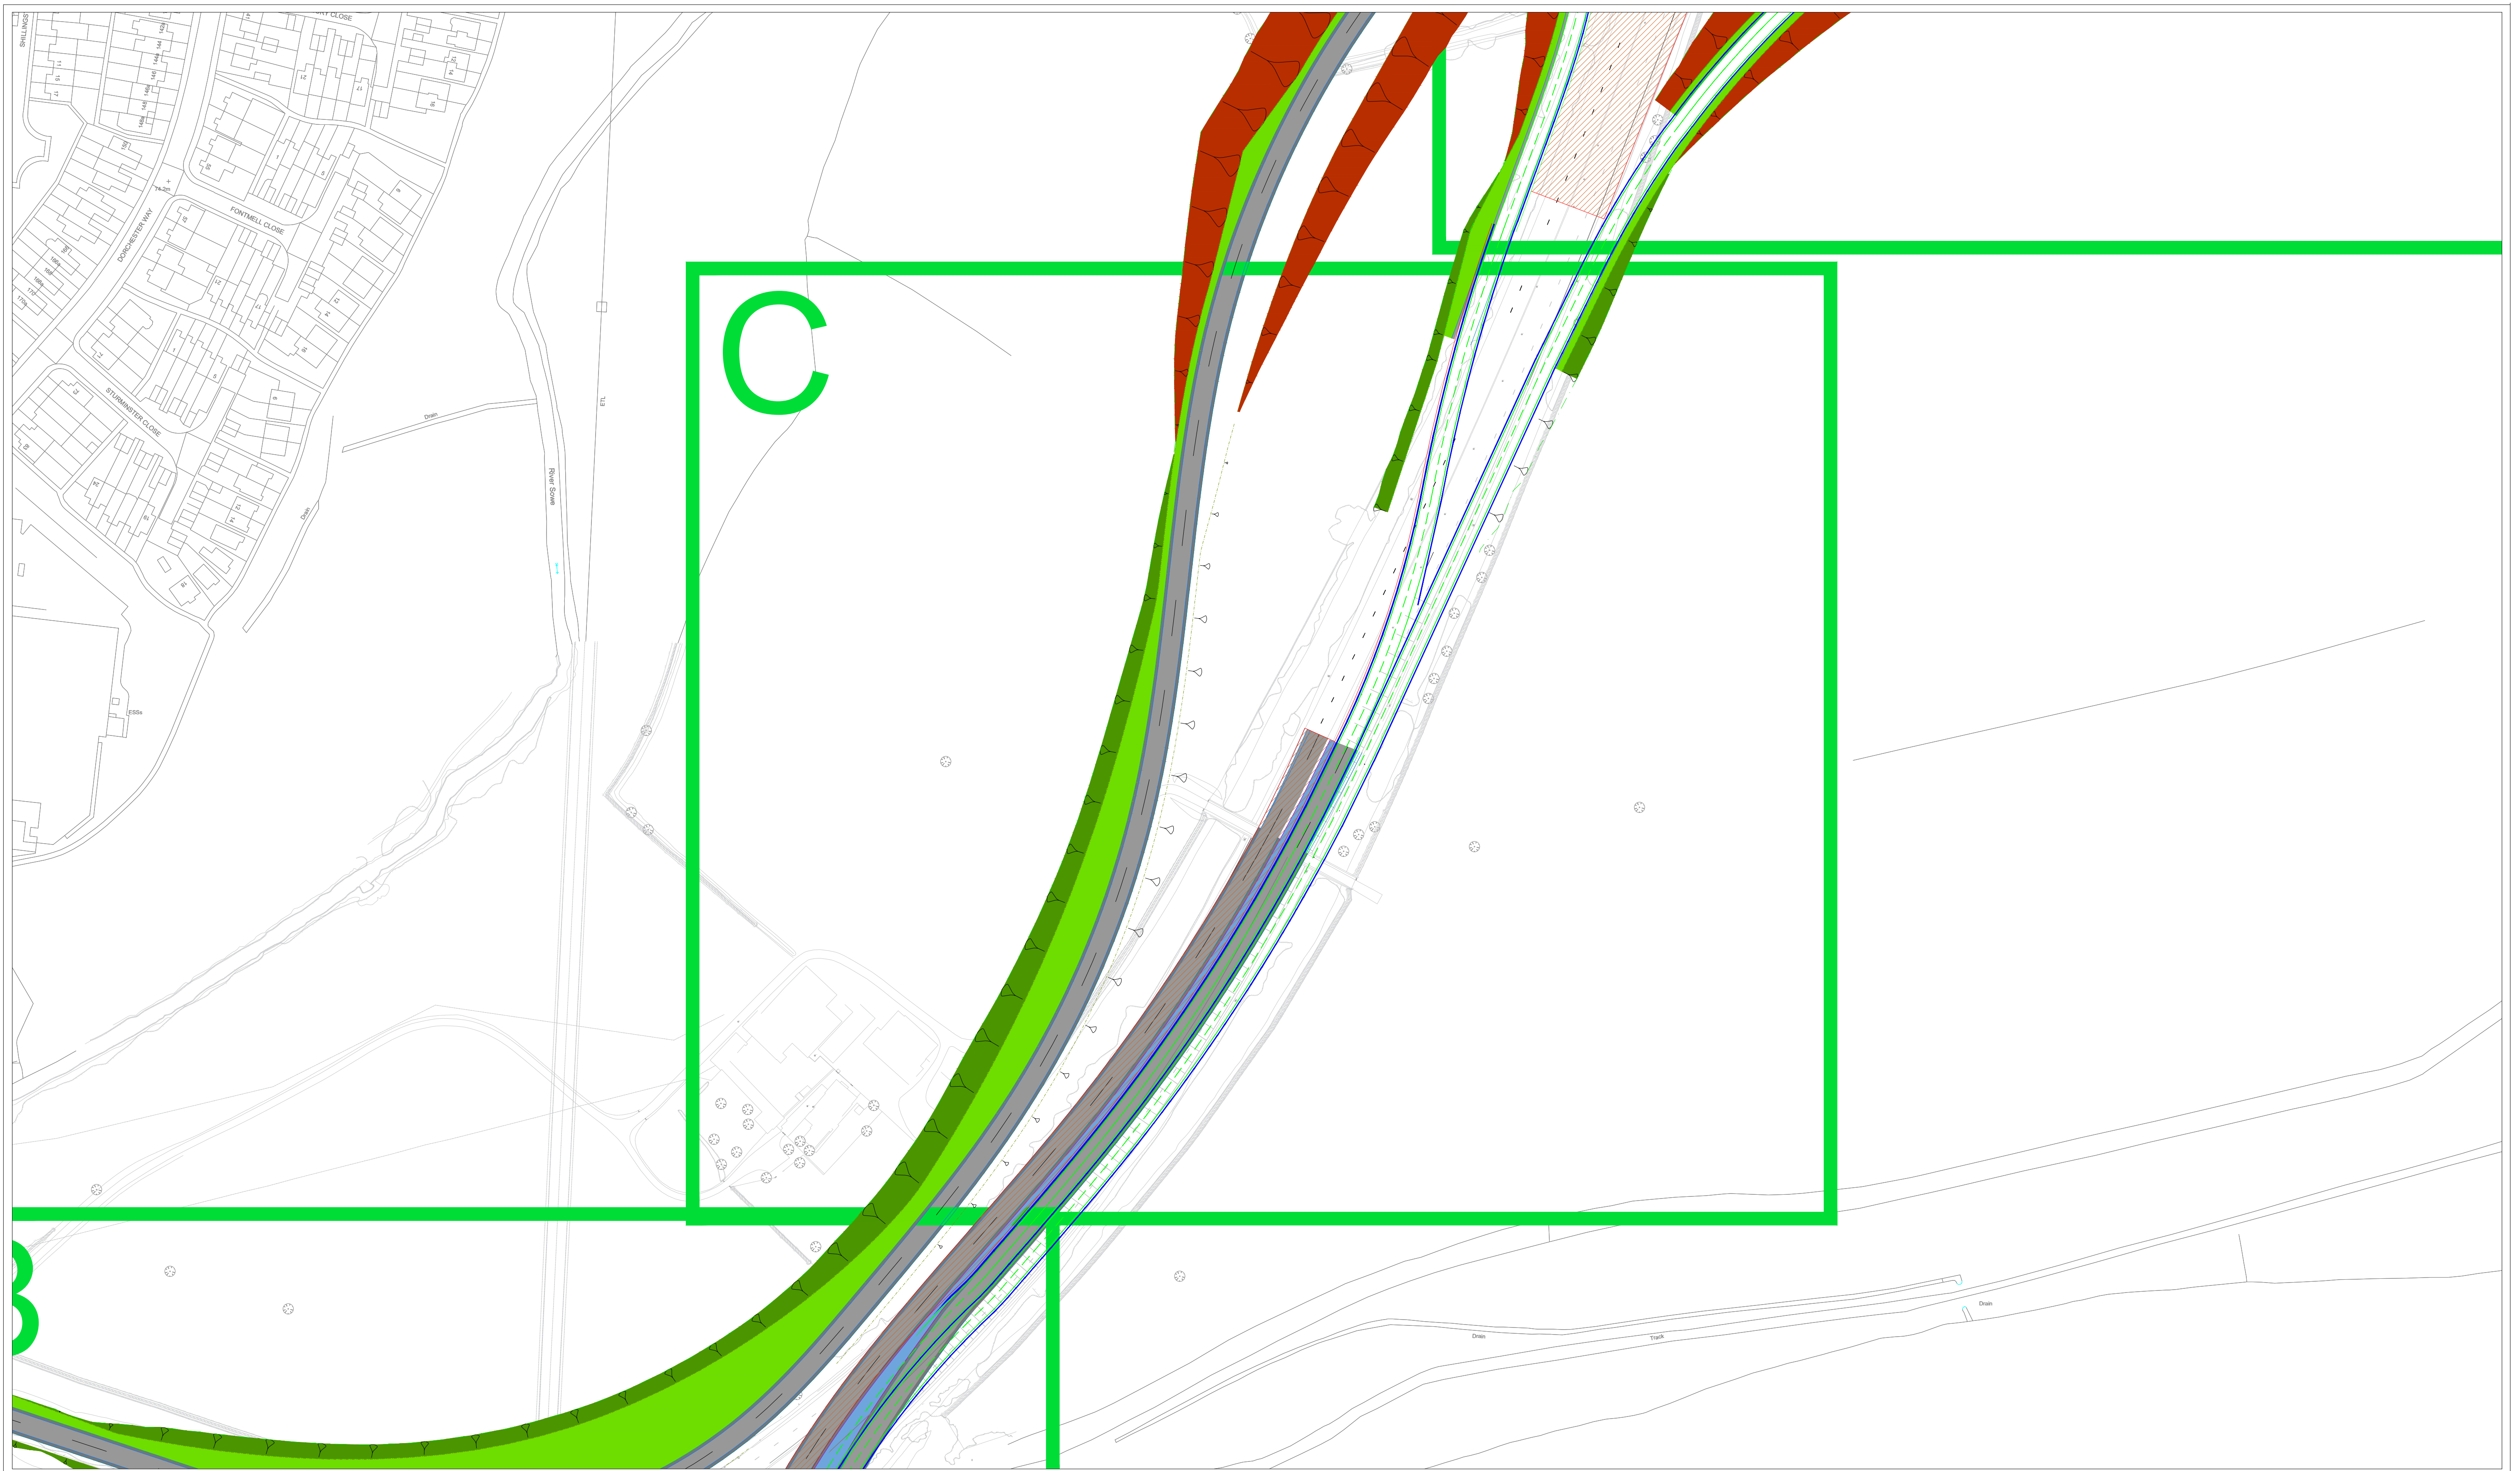

Client:

Project Title: **A46 Walsgrave Junction Upgrade**
 Drawing Title: **Option 11 Phase 3 - C**
 Drawing No.: **DRAFT OUTLINE 001**

Revision details		
Revision	Sheet No.	4 of 5
Revised by:	Rev:	Date:

Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>
For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>
Drawn by:	Ed Menear	Date:	17/08/21
Verified by:		Date:	
Validation by:		Date:	
Original size	A1	Scale	NTS


Technical Support

Designer Checklist No:	xxx
Technical Note & Design Commentary No:	xxx
Associated Risk Assessment No:	xxx
Layer Register No:	xxx
DWG File Number No:	xxx

IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX

HAZARD/RISK	HIGH/MED/LOW

KEY:

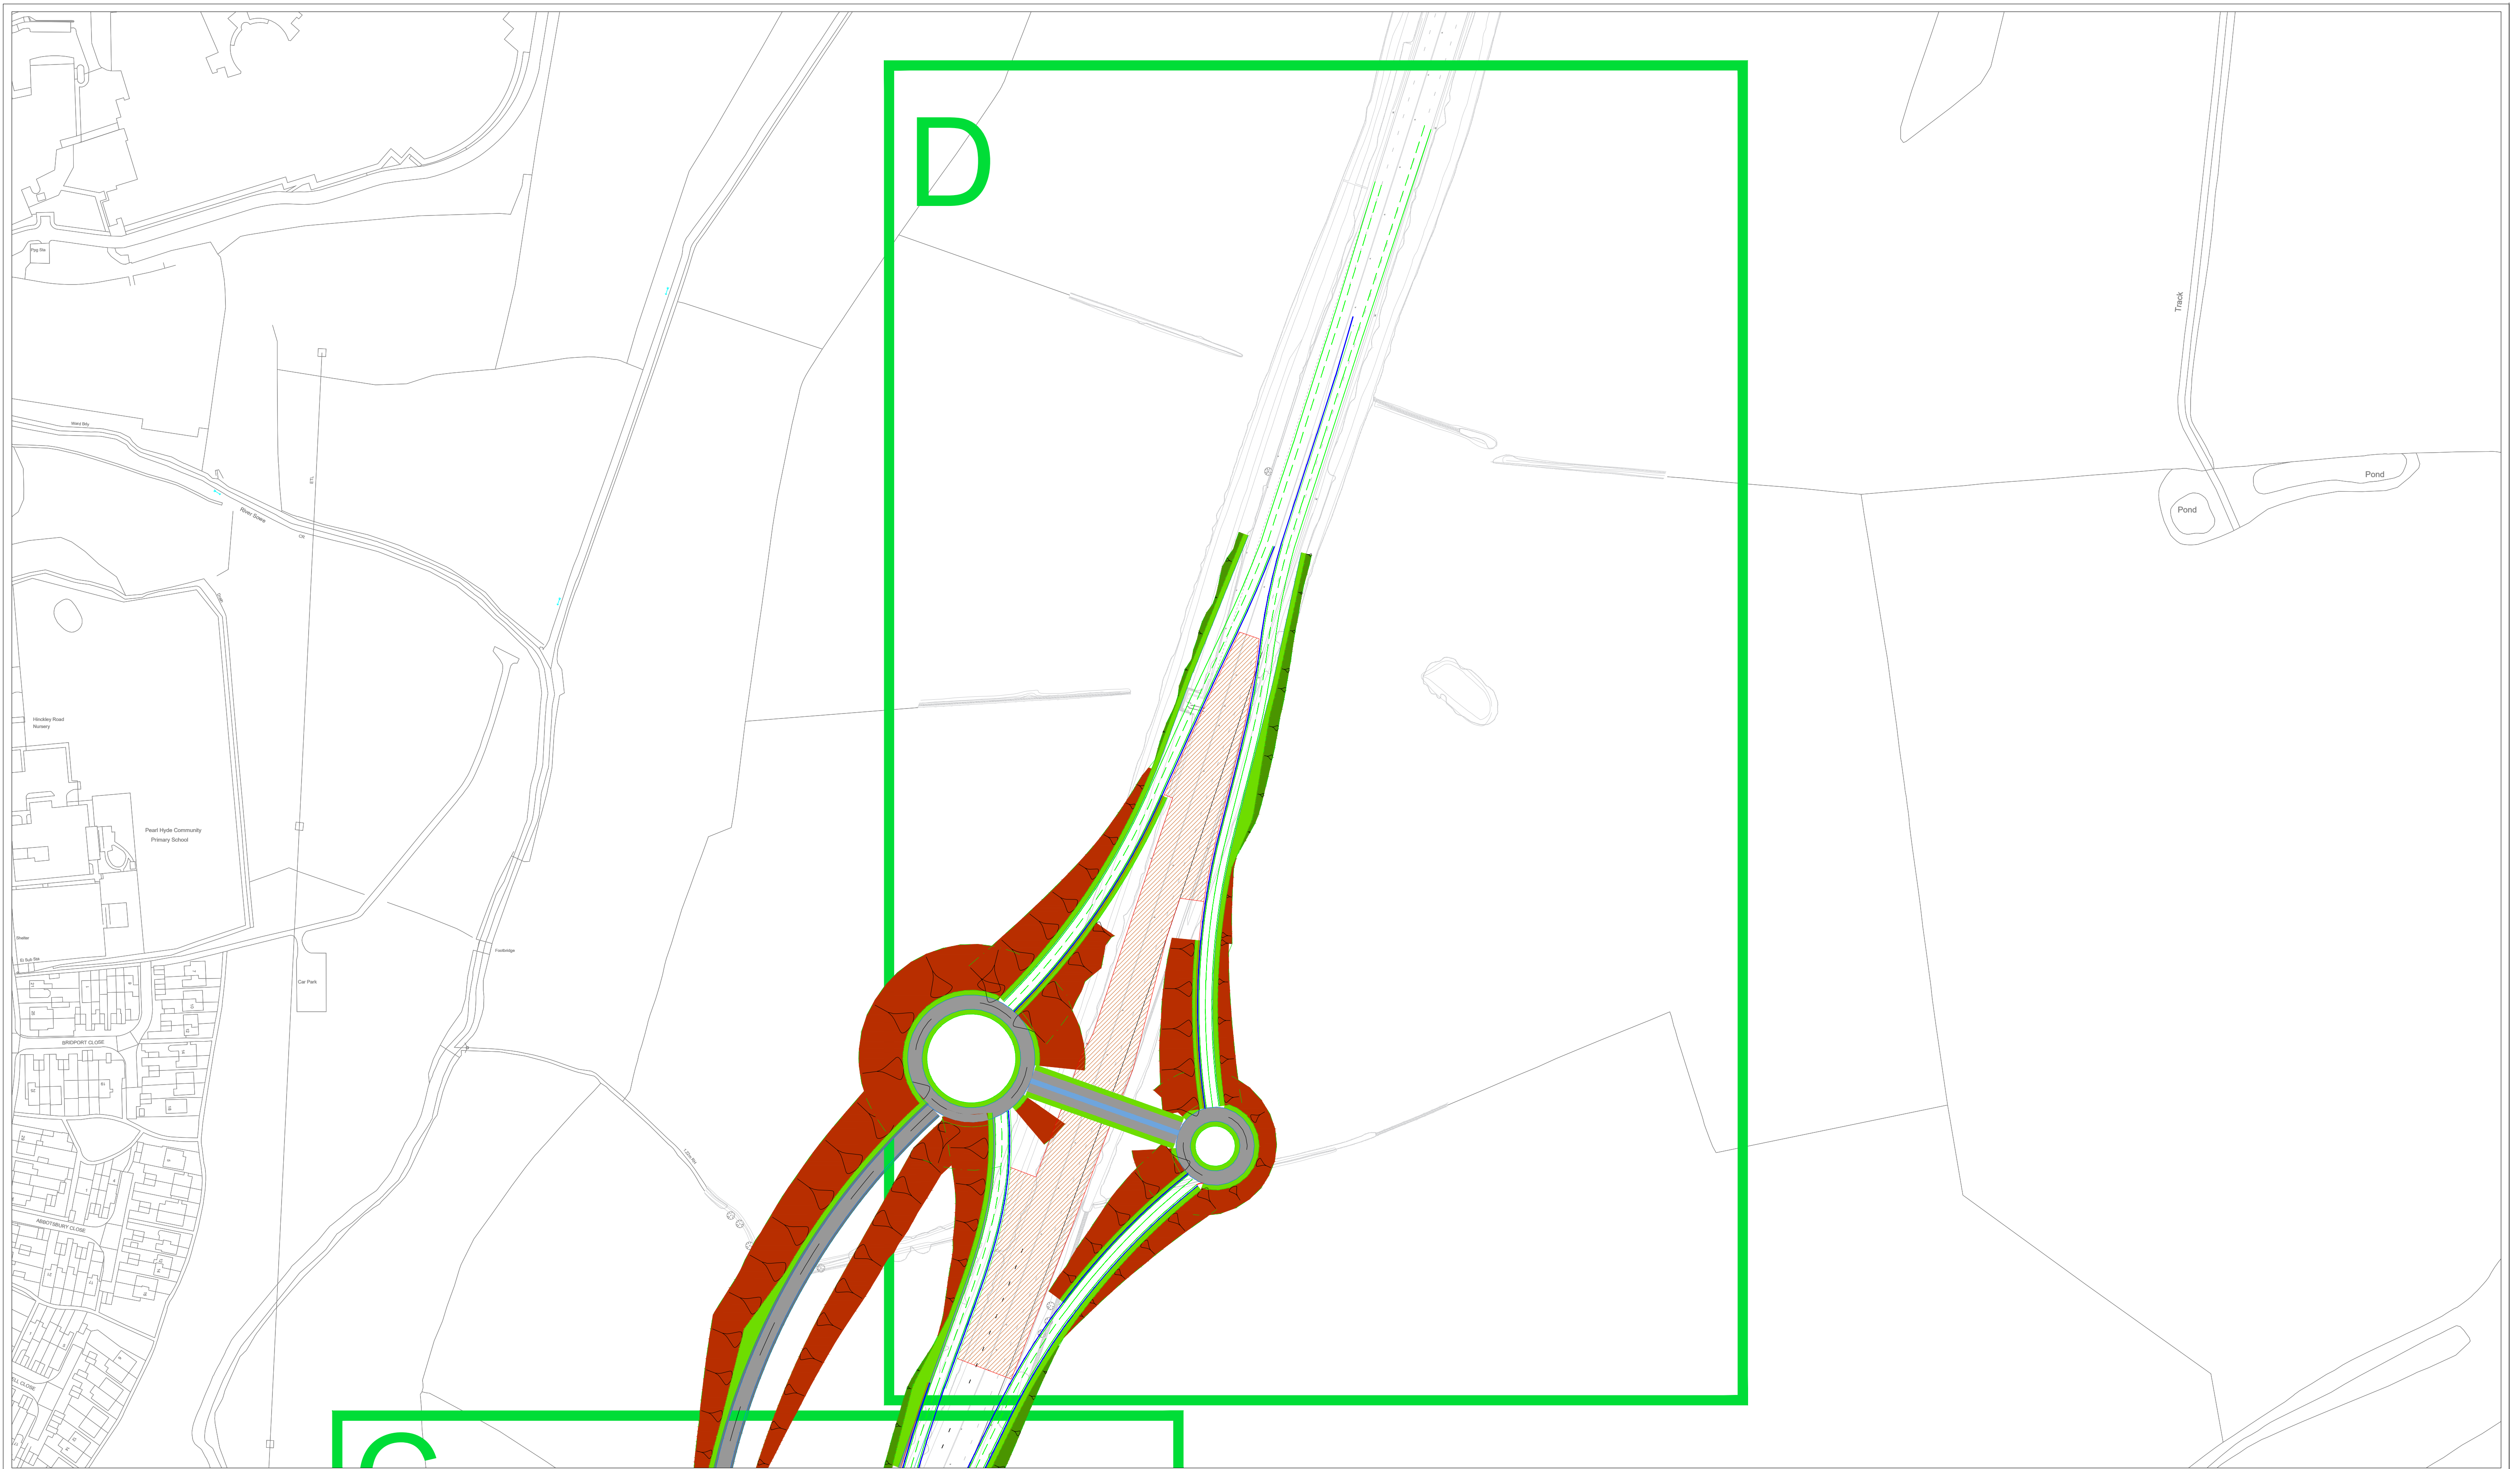

Client:

Project Title: **A46 Walsgrave Junction Upgrade**
 Drawing Title: **Option 11 Phase 3 - D**
 Drawing No.: **DRAFT OUTLINE 001**

Preliminary For approval
 For comment Final Design
 Drawn by: **Ed Menear** Date: **17/08/21**
 Verified by: _____ Date: _____
 Validation by: _____ Date: _____
 Original size **A1** Scale **NTS**

IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX

HAZARD/RISK	HIGHMEDLOW
1	

KEY:

Revision details		
Revision	Sheet No.	5 of 5
Revised by:	Rev:	Date:


Technical Support
 Designer Checklist No: xxx
 Technical Note & Design Commentary No: xxx
 Associated Risk Assessment No: xxx
 Layer Register No: xxx
 DWG File Number No: xxx

A



check widening detail at brinklow - para width if unachievable, the remaining will get picked up in weekend closure

Client:





Project Title:	A46 Walsgrave Junction Upgrade	
Drawing Title:	Option 6 Overview - A	
Drawing No.:	DRAFT OUTLINE 001	
Revision details		
Revision	Sheet No.	2 of 5
Revised by:	Rev:	Date:

Preliminary	<input checked="" type="checkbox"/>	For approval
For comment	<input checked="" type="checkbox"/>	Final Design
Drawn by:	Ed Menear	Date: 01/02/21
Verified by:		Date:
Validation by:		Date:
Original size	A1	Scale NTS
Technical Support		
Designer Checklist No:	xxx	
Technical Note & Design Commentary No:	xxx	
Associated Risk Assessment No:	xxx	
Layer Register No:	xxx	
DWG File Number No:	xxx	

IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX

HAZARD/RISK	HIGH/MED/LOW

KEY:

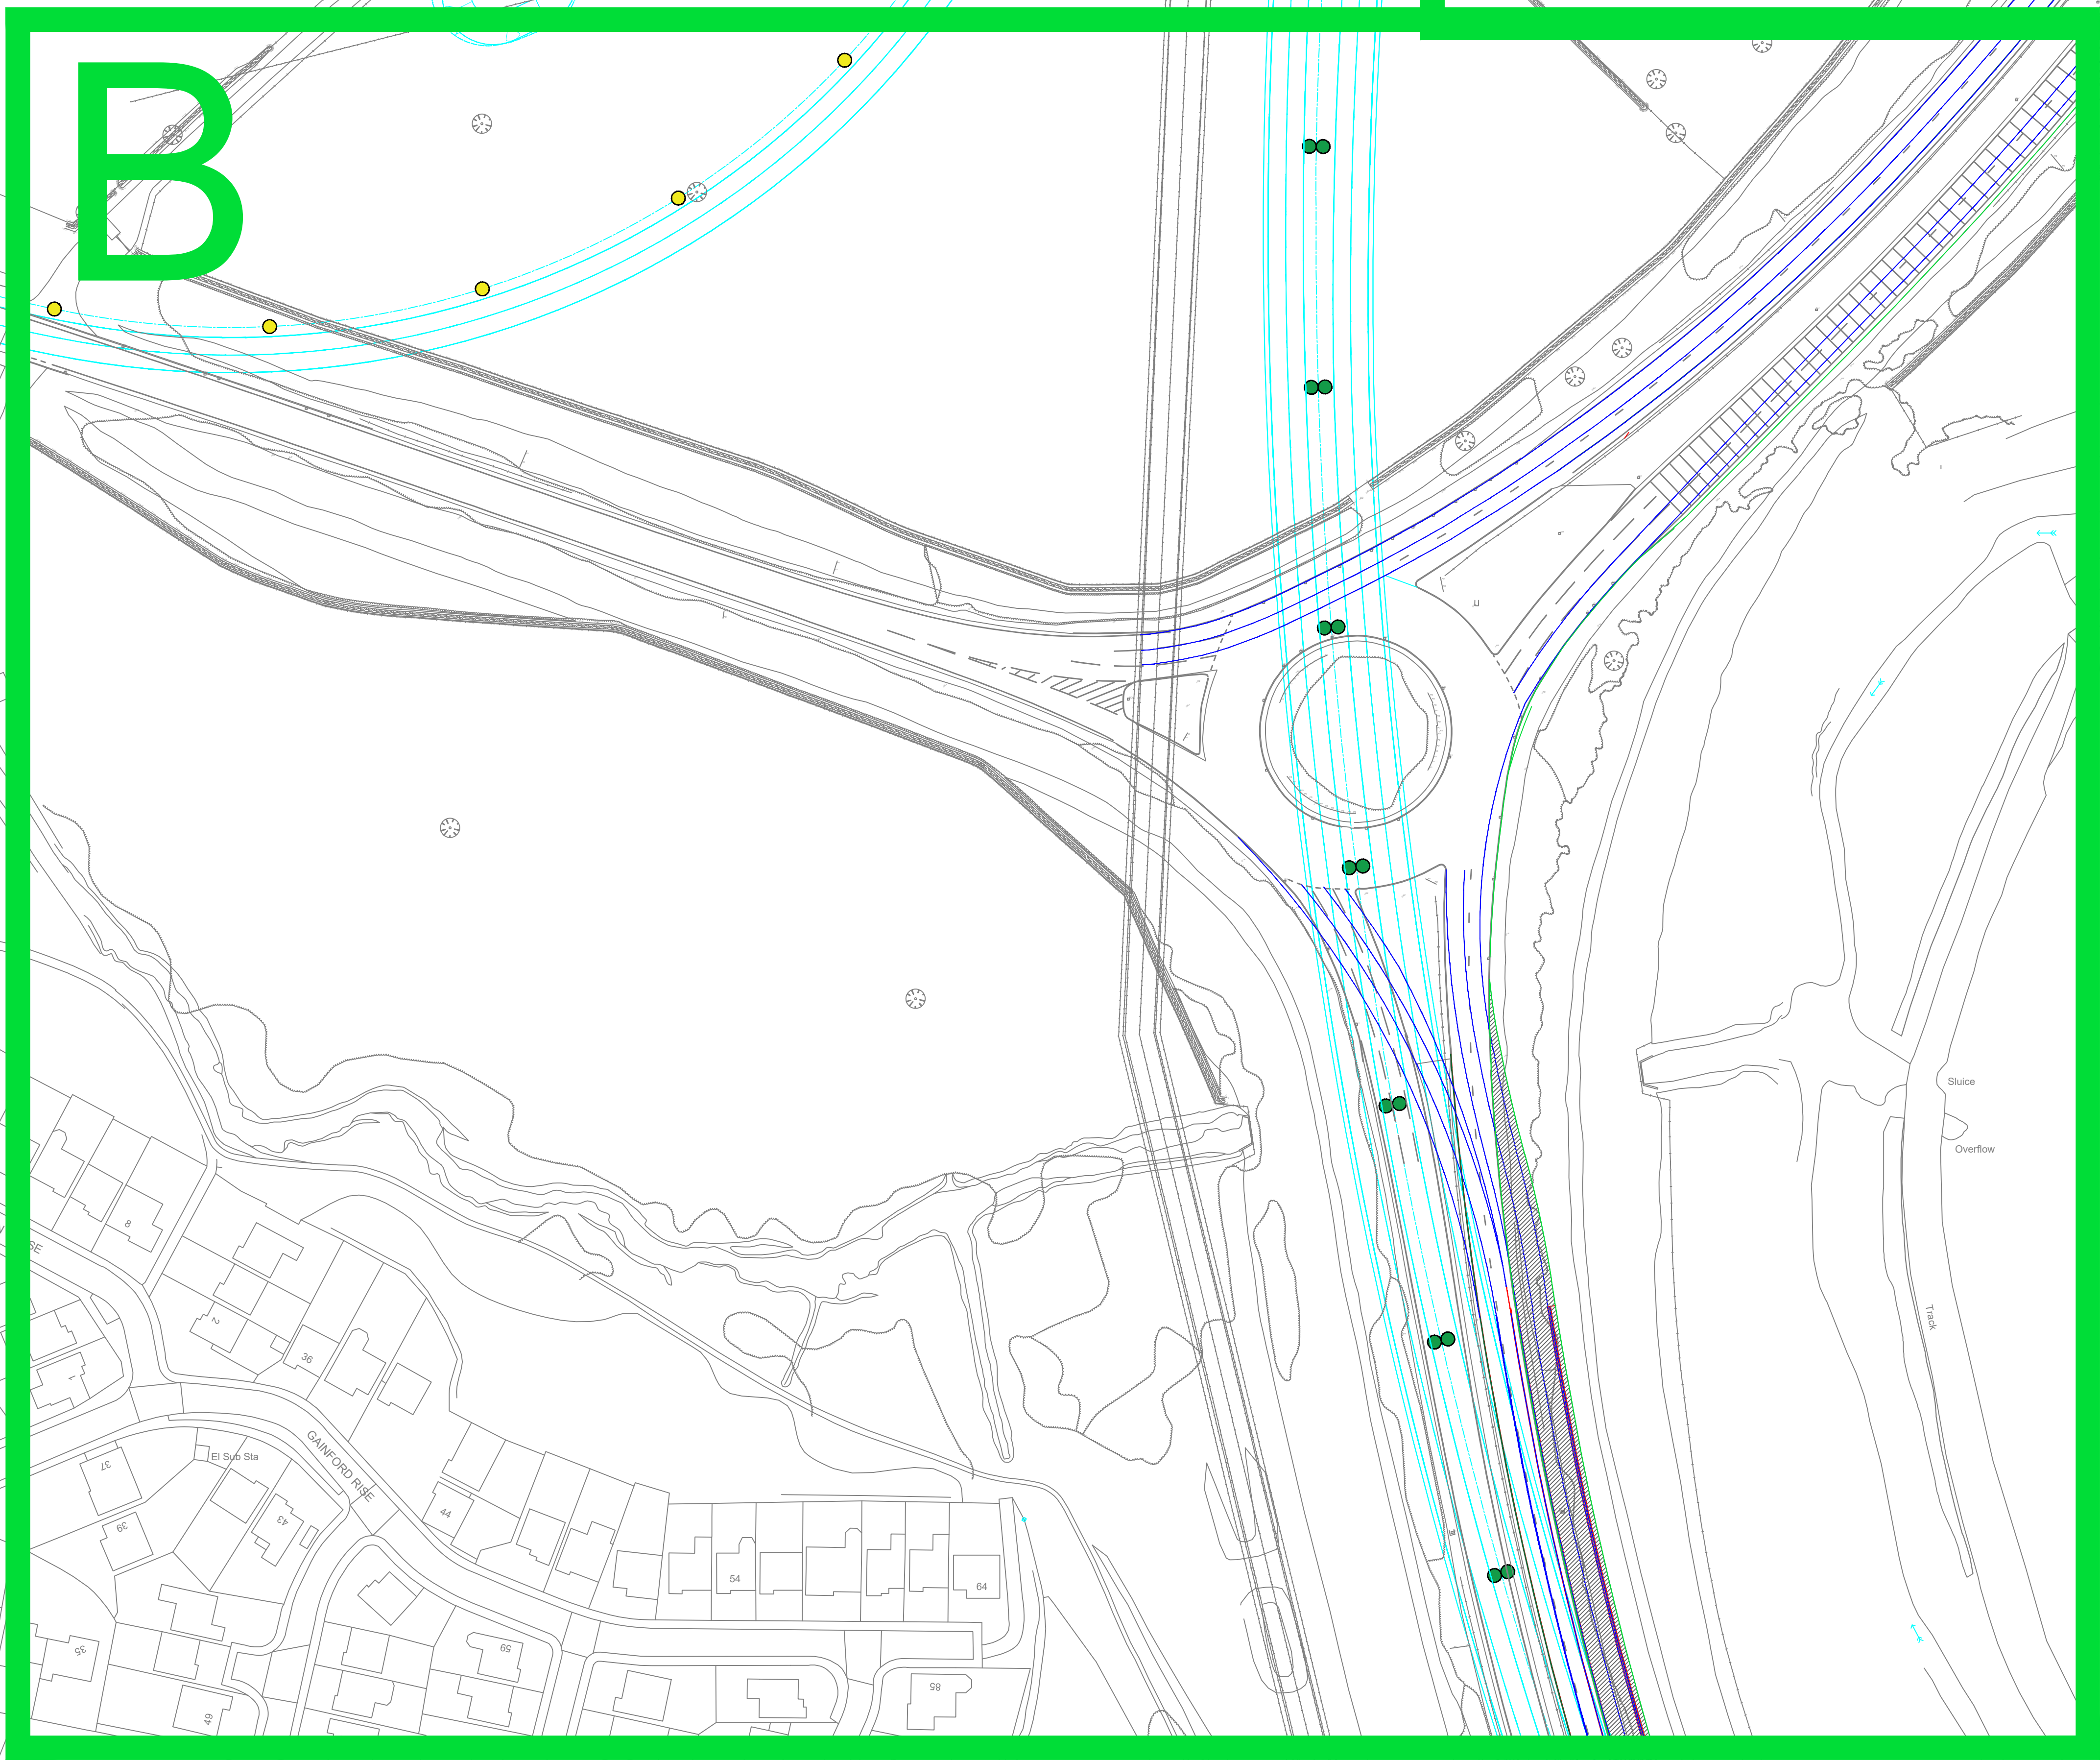

Project Title: A46 Walsgrave Junction Upgrade		
Drawing Title: Option 6 Overview - B		
Drawing No.: DRAFT OUTLINE 001		
Revision details		
Revision	Sheet No.	3 of 5
Revised by:	Rev:	Date:

Preliminary	<input checked="" type="checkbox"/>	For approval	<input type="checkbox"/>
For comment	<input checked="" type="checkbox"/>	Final Design	<input type="checkbox"/>
Drawn by:	Ed Menear	Date:	01/02/21
Verified by:		Date:	
Validation by:		Date:	
Original size	A1	Scale	NTS
Technical Support			
Designer Checklist No:	xxx		
Technical Note & Design Commentary No:	xxx		
Associated Risk Assessment No:	xxx		
Layer Register No:	xxx		
DWG File Number No:	xxx		



IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	
HAZARD/RISK	HIGH/MED/LOW

KEY:

Client:




884

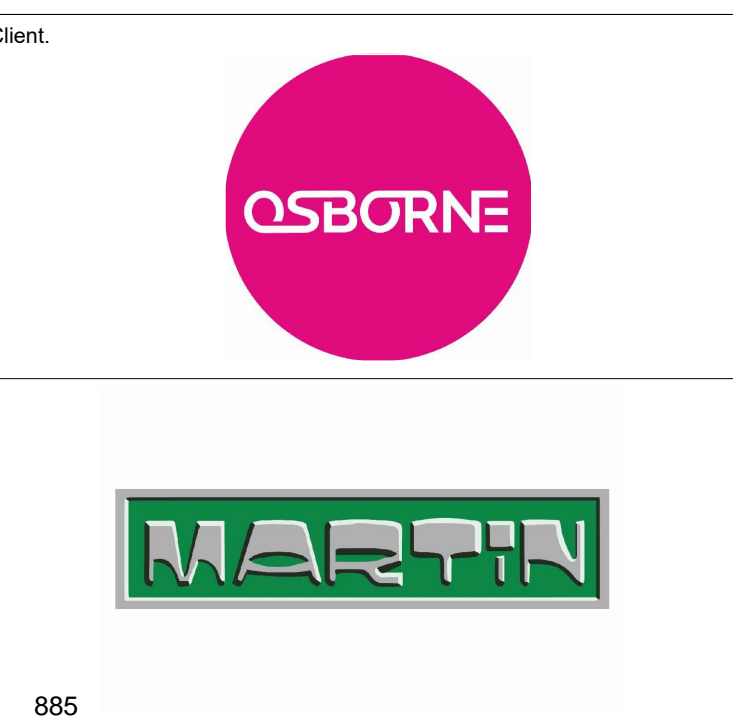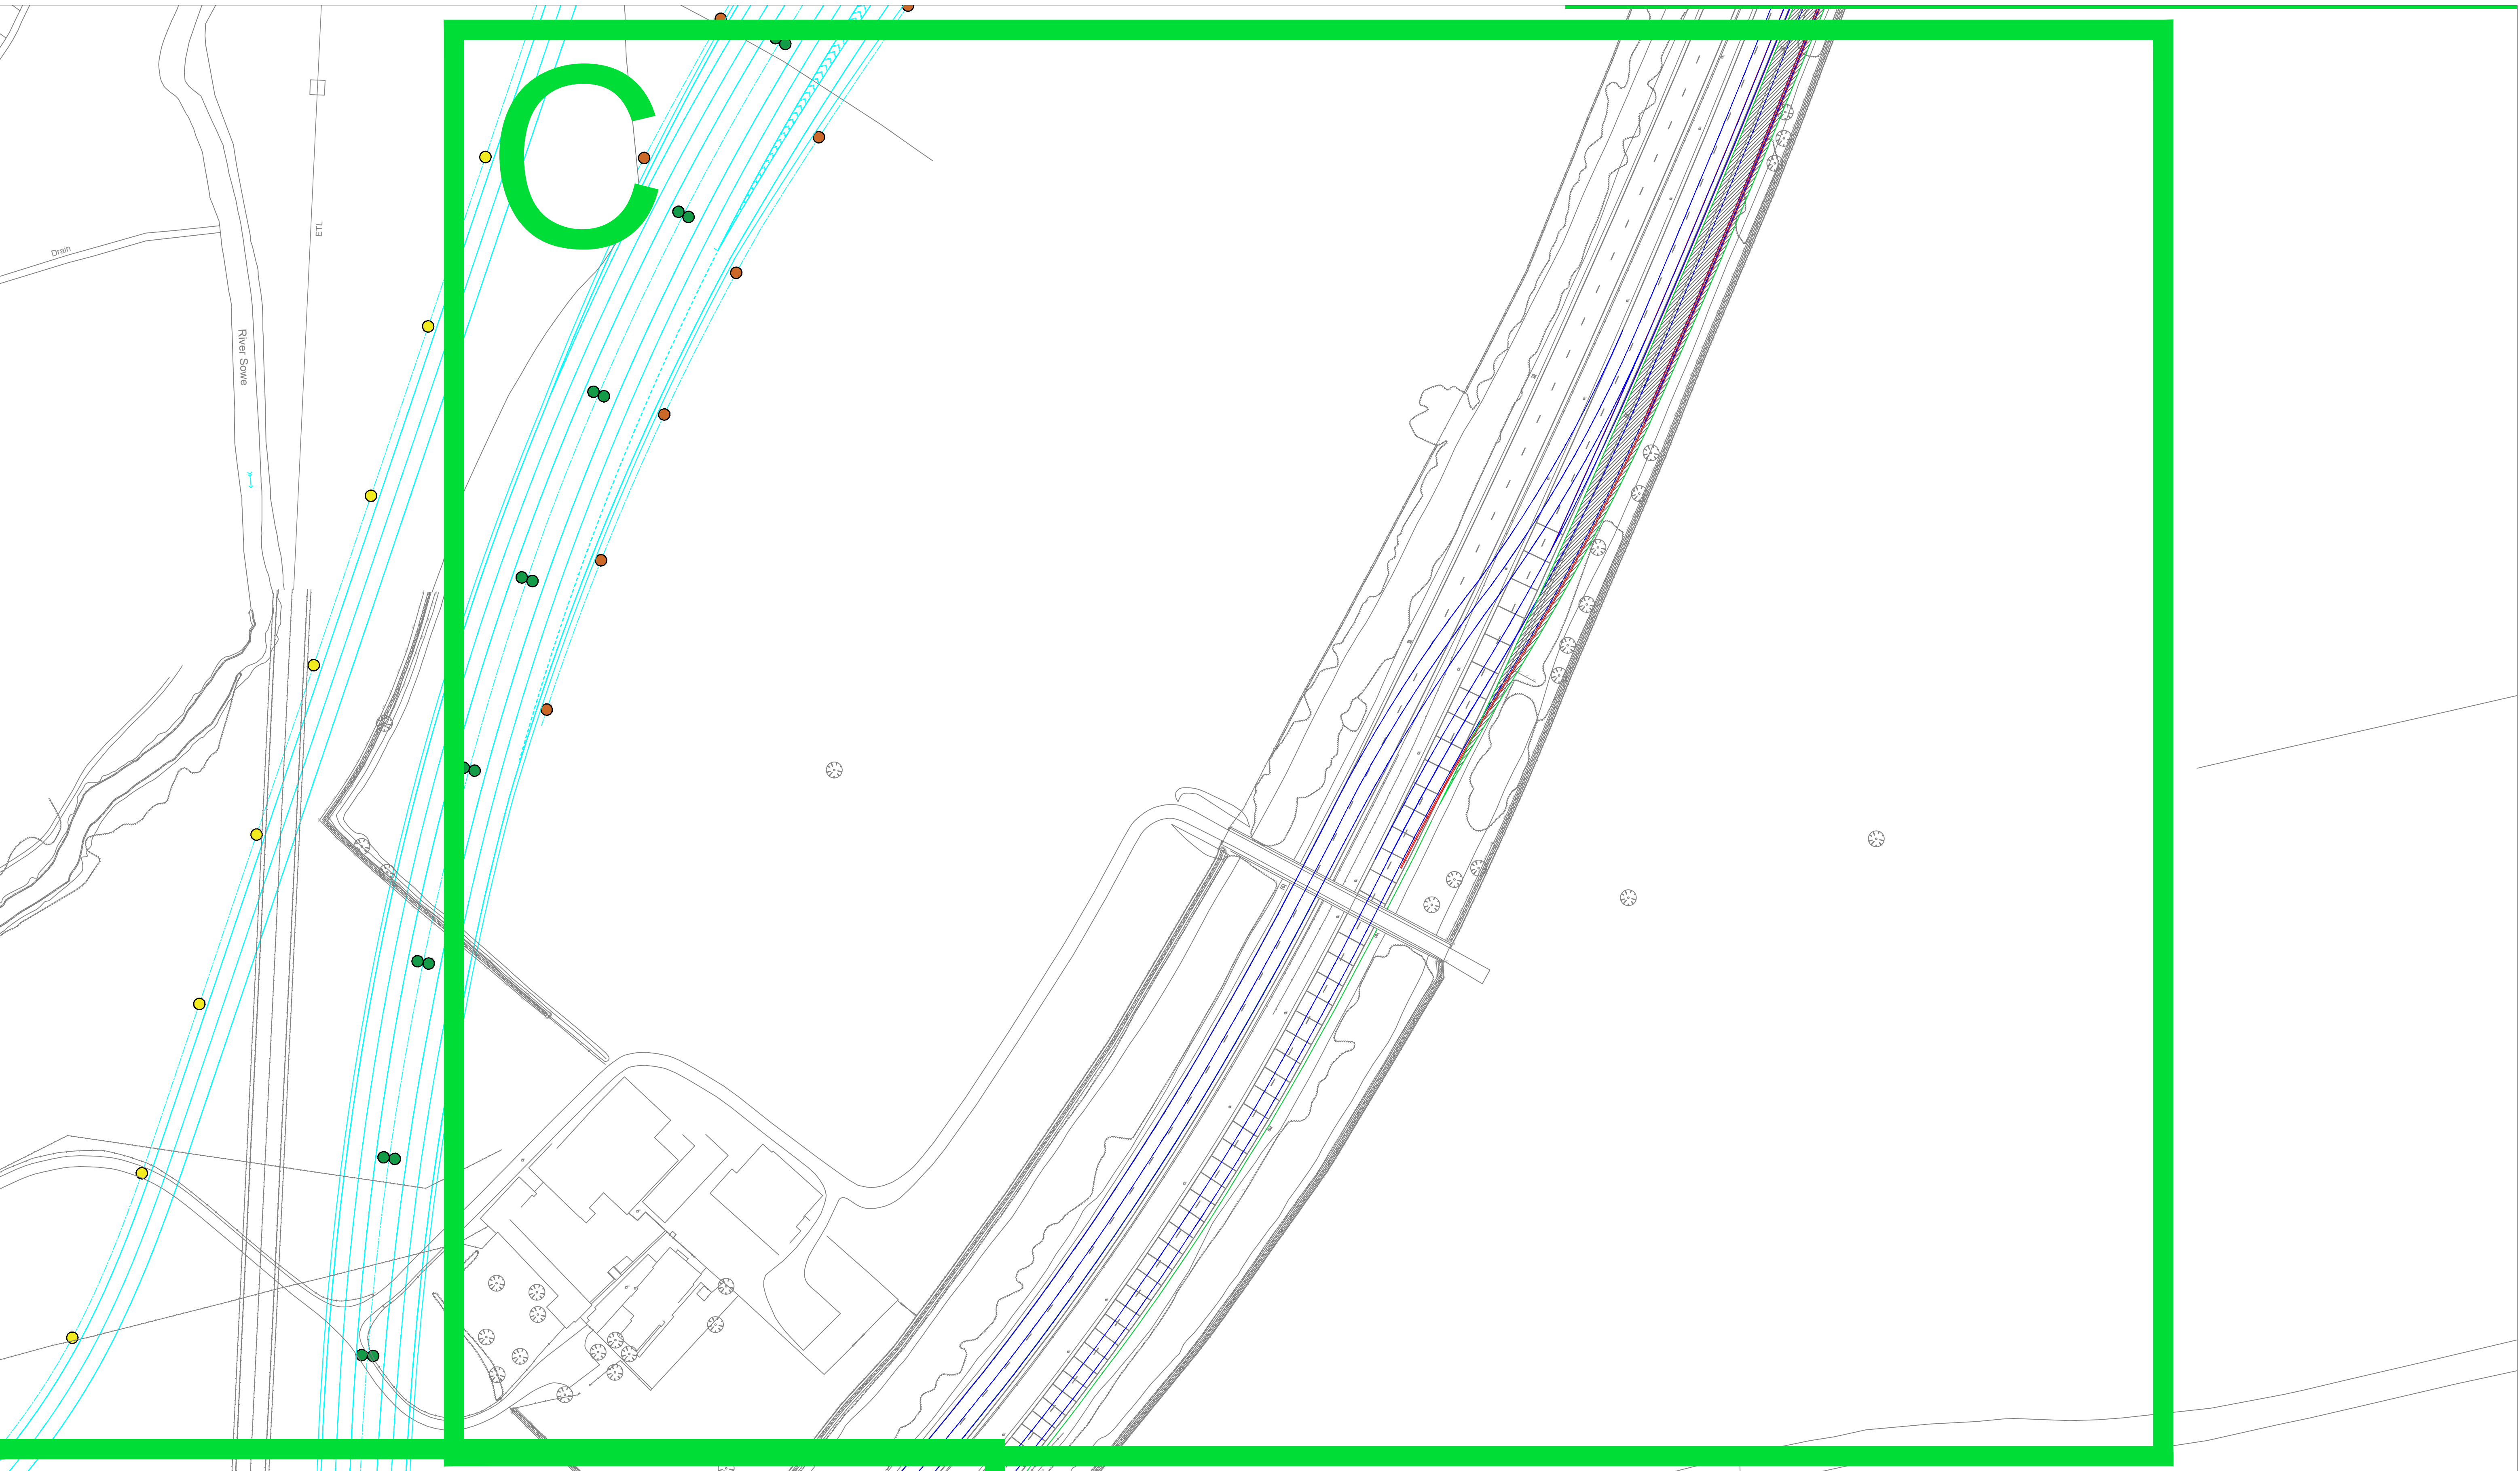

Project Title:	A46 Walsgrave Junction Upgrade		
Drawing Title:	Option 6 Overview - C		
Drawing No.:	DRAFT OUTLINE 001		
Revision details			
Revision	—	Sheet No.	4 of 5
Revised by:	Rev:	Date:	

Preliminary	<input checked="" type="checkbox"/>	For approval	
For comment	<input checked="" type="checkbox"/>	Final Design	
Drawn by:	Ed Menear	Date:	01/02/21
Verified by:		Date:	
Validation by:		Date:	
Original size	A1	Scale	NTS
Technical Support			
Designer Checklist No:	xxx		
Technical Note & Design Commentary No:	xxx		
Associated Risk Assessment No:	xxx		
Layer Register No:	xxx		
DWG File Number No:	xxx		

IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, PLEASE NOTE THE FOLLOWING SIGNIFICANT RESIDUAL RISKS IN THE HAZARD/RISK BOX	
HAZARD/RISK	HIGH/MED/LOW

KEY:	

